


Work continues to progress on the Stormwater/Resilience Master Plan throughout vulnerable neighborhoods in the City. Updated project progress is provided below. Work continues on planning efforts associated with the Tranche 2 neighborhoods.

Neighborhood	Project Status
1a Edgewood	Construction substantially complete, final completion anticipated for late March 2024
1b Osceola Creek Dredging (Edgewood)	Construction 75% complete
2a River Oaks (Underground Utilities)	Construction substantially complete
2b River Oaks (Pump Stations)	In construction
3 Durrs	Construction contract awarded on 2/6/2024, Pre-construction activities have commenced
4 Dorsey-Riverbend	Construction contract to be awarded in April 2024
5 Progresso Village	Design being updated; Bidding Fourth Quarter 2024
6 Southeast Isles	Design being updated; Bidding Third Quarter 2025
6a Merle Fogg Park Seawall Replacement	In Construction
6b Southeast Isles Seawalls Replacement	In Construction
7 Victoria Park	Design being updated; Bidding First Quarter 2025
8 Melrose Manors/ Riverland Civic	In Design; estimated design completion Fall 2025



Stormwater improvements in the Edgewood Neighborhood are almost complete! New stormwater infrastructure has been added to one of the most vulnerable areas in the City. This infrastructure includes catch basins, gravity piping, exfiltration trenches, swales, outfalls, and tidal valves. The Edgewood system will be fully functional once the River Oaks Pump Stations become operational. The Edgewood project is anticipated to be complete by the end of March, **five months ahead of schedule!**

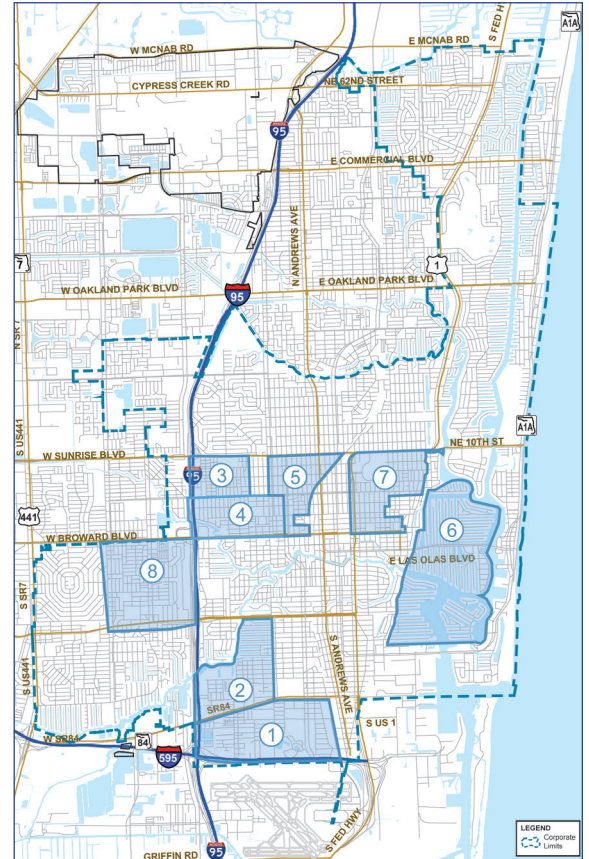
