


Work continues to progress on the Stormwater/Resilience Master Plan throughout vulnerable neighborhoods in the City. Updated project progress is provided below. Work continues on planning efforts associated with the Tranche 2 neighborhoods, including updates to the City's existing stormwater model simulating current and future conditions to direct stormwater improvements.

Neighborhood	Project Status
1a Edgewood	Final completion anticipated June 2024
1b Osceola Creek Dredging (Edgewood)	Maintenance dredging 85% complete
2a River Oaks (Underground Utilities)	Construction substantially complete
2b River Oaks (Pump Stations)	In Construction
3 Durrs	In Construction
4 Dorsey-Riverbend	Construction contract awarded 4/2/2024, Pre-Construction activities have commenced
5 Progresso Village	Design being updated; Bidding Fourth Quarter 2024
6 Southeast Isles	Design being updated; Bidding Third Quarter 2025
6a Merle Fogg Park Seawall Replacement	Construction substantially complete, Final Completion anticipated June 2024
6b Southeast Isles Seawalls Replacement	Construction substantially complete, Final Completion anticipated June 2024
7 Victoria Park	Design being updated; Bidding First Quarter 2025
8 Melrose Manors/ Riverland Civic	In Design; estimated design completion Fall 2025



The Southeast Isles Seawalls Project is substantially complete! Work performed under the Southeast Isles Seawalls project included the replacement of five seawalls and their associated catch basins and outfalls. All outfalls were equipped with an inline check valve to prevent tidal flooding.

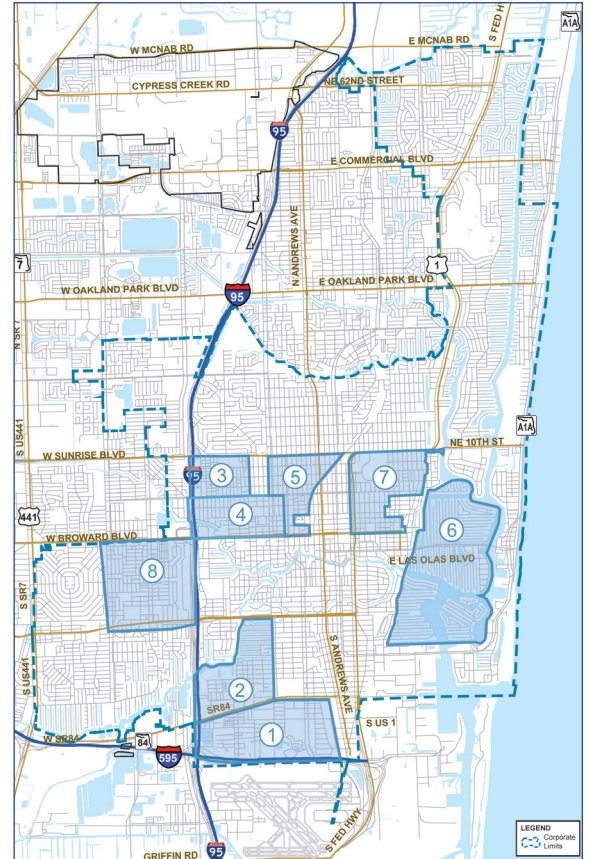
