

CITY OF FORT LAUDERDALE

OFFICE OF THE CITY AUDITOR

*Carr, Riggs and Ingram (CRI) Forensic Examination of the Rio Vista
Restoration Project*

Report #21/22-03

December 7, 2021



Carr, Riggs & Ingram, LLC
500 Grand Boulevard
Suite 210
Miramar Beach, FL 32550

850.837.3141
850.654.4619 (fax)
CRICpa.com

November 29, 2021

Mr. John Herbst, CPA, CGFO, CGMA
City Auditor
City of Fort Lauderdale, Florida
100 N. Andrews Avenue
Fort Lauderdale, FL 33301

Re: Forensic Examination of the Rio Vista Restoration Project

Dear Mr. Herbst:

Our firm was engaged to perform an inquiry concerning the City of Fort Lauderdale, Florida's (City) Rio Vista Restoration Project. This inquiry was predicated on the discovery that certain City policies and procedures did not appear to have been followed for this project. Attached is Carr, Riggs & Ingram, LLC's Forensic Examination Report detailing the procedures performed and the resulting findings.

We have performed this engagement in accordance with the Statement on Standards for Forensic Services No. 1 as promulgated by the American Institute of Certified Public Accountants (AICPA). While our work involved analysis of accounting records, our engagement did not constitute an audit in accordance with generally accepted auditing standards, an examination of internal controls, or any other attestation or review service in accordance with standards established by the AICPA. Had other procedures been performed, other matters may have come to our attention that may have affected the findings reported herein.

This report is intended solely for the use of the City and should not be used for any other purpose without prior permission from CRI. We have no obligation, but reserve the right, to update this report for information that comes to our attention after the date of this report.

Sincerely,

Carr, Riggs & Ingram, LLC

Carr, Riggs & Ingram, LLC
Certified Public Accountants



**City of Fort Lauderdale, Florida
Rio Vista Restoration Project**

**Forensic Examination Report and
Supplementary Information**

November 29, 2021



**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Table of Contents**

Executive Summary	1
Forensic Examination Report	
Background	2
Scope	3
Approach	4
Expert Qualifications	4
Summary of Procedures Performed	5
Source Documentation	6
Finding 1 – Policies and Procedures	6
Finding 2 – Understanding of the Rio Vista Restoration Project	7
Finding 3 – Supporting Documentation Analysis	16
Finding 4 – Internal Control Override Analysis	25
Conclusion	27
Supplementary Information	
Schedule A – Summary of Relevant Communications	29
Appendix A – Expert Qualifications	
Appendix B – Source Documentation	
Appendix C – Management Responses (City Manager Memorandum 21-38)	

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Executive Summary

Executive Summary

Carr, Riggs & Ingram, LLC (CRI) was engaged to perform an inquiry into the City of Fort Lauderdale, Florida's (City) Rio Vista Restoration Project. This inquiry was predicated on the discovery that City policies and procedures did not appear to have been followed for the Rio Vista Restoration Project and City concerns that internal controls may have been overridden on this project.

CRI performed certain procedures on the City's books and records for December 1, 2019 through August 31, 2021 (review period). These procedures included, but were not limited to, interviews with key City personnel and analysis of supporting documentation including certain City personnel's electronic data. Summaries of CRI's major findings, based upon the investigative procedures performed, are listed below.

- **Contract/Procedures Conflicting Interpretations**

The City has taken broad or conflicting interpretations on the administrative renewal of master contracts as well as the uses of master contracts. This appears to have included administratively renewing contracts for additional funds not clearly authorized by the City Commission. The City has also utilized line item master contracts for unrelated projects not included in the master contract scope. These interpretations occurred with other projects prior to the Rio Vista Restoration Project and these interpretations may have arisen in prior City administrations. Refer to Findings 2 and 3.

- **Commissioner Sorensen Directed City Staff/Vendors**

Commissioner Sorensen's frequent communications with lower level City staff and certain communications with City staff/vendors do not reflect mere Commissioner inquiries. Rather, based on the volume and frequency of these communications, Commissioner Sorensen directed City staff/vendors during the Rio Vista Restoration Project. It does not appear that Commissioner Sorensen's direction of City staff/vendors was done with malicious intent. It was done in an apparent effort to assist the Rio Vista residents in his District, who had endured the sewer breaks. The City was unaware of City related communications by Commissioner Sorensen on his personal cell phone and certain records may not have been retained as required. Refer to Findings 2, 3 and 4.

- **Public Works Director Overrode City Policies and Procedures**

The former Public Works Director, Raj Verma, directed City staff to bypass the City's policies and procedures in relation to the Rio Vista Restoration Project. Mr. Verma disregarded City policies and procedures in the interest of getting projects completed and created a poor "tone at the top" of the Public Works Department. As such, Mr. Verma directed City staff to significantly expand the Rio Vista Restoration Project's scope without proper approval pursuant to City policies and procedures. Mr. Verma also directed staff not to prepare/submit a change order in relation to the expanded scope until after the work was predominately completed. Mr. Verma in effect encouraged communications between City staff and Commissioner Sorensen. Refer to Findings 1, 2, 3 and 4.

We recommend that the City review and implement the 5 recommendations in our report for improving the City's procurement internal controls as soon as possible. The procedures performed by CRI and the resulting findings are discussed in detail within the Forensic Examination Report.

City of Fort Lauderdale, Florida Rio Vista Restoration Project Forensic Examination Report

Background

The City of Fort Lauderdale, Florida (City) was established in 1911 and is located in Broward County, Florida. The City provides a wide range of services for the residents of Fort Lauderdale. These services include police protection, fire-rescue services, parks and recreation programs, water, wastewater collection and treatment, sanitation services, parking and street maintenance.


The power and authority to set policies for the City is vested in the City Commission, which is elected by the citizens of Fort Lauderdale. The City Commission consists of five members. The Mayor is elected at-large and the remaining four commissioners are elected by individual districts. The City operates under a commission-manager form of government. The City Commission appoints four charter officers and delegates certain duties and responsibilities to these charter officers. These charter officers include a City Manager, a City Attorney, a City Clerk and a City Auditor.

The City Manager is responsible for the administration of the City and its daily operations. The City Manager is generally responsible for hiring the various City department directors. One of the City's departments is the Public Works Department. This department has three divisions, which include engineering, sustainability and utilities. The Engineering Division provides project management for improvements to the City's infrastructure and the Sustainability Division oversees the implementation of the City's Sustainability Action Plan and other essential environmental services. The Utilities Division is responsible for maintaining the City's water and wastewater infrastructure.

On or around December 10, 2019, there was a break in the City's sewer main line, which consisted of a 54-inch sewer pipe. The sewer main line carries all of the sewer flow from the City and five other municipalities to the George T. Lohmeyer Regional Wastewater Treatment Plant. The sewer break occurred at or around 1030 Ponce De Leon Drive in the Rio Vista neighborhood. On or about December 20, 2019, a separate break in the City's sewer main line occurred. This occurred at or around 909 S.E. 10th Street in the Rio Vista neighborhood. Due to the critical nature of the sewer pipe breaks, over 200 million gallons of untreated waste/sewage flowed into the Rio Vista neighborhood and the surrounding waterways. The sewer breaks impacted two City parks located in the Rio Vista neighborhood: Hector Park and Virginia S. Young Park. The Rio Vista neighborhood is a high-end residential area that has an active voluntary civic association, the Rio Vista Civic Association. The Rio Vista neighborhood is part of City District Four, which is represented by Commissioner Ben Sorensen. A Google map overview of the sewer breaks and their proximity to the City parks is presented on the following page.

The City issued an emergency purchase order to David Mancini & Sons, Inc. for the emergency repairs and clean-up related to the sewer line breaks. David Mancini & Sons, Inc. was also engaged by the City to replace the southern portion of the sewer main line. In or around April 2020, the City's Public Works Department initiated the restoration process for Hector Park and Virginia S. Young Park (Rio Vista Restoration Project) and utilized a City contractor, Hinterland Group, Inc. (Hinterland). In or around June 2021, the Public Works Department submitted a change order for \$871,486.50 related to a task order issued to Hinterland for the Rio Vista Restoration Project. The City's Finance Department began questioning the submitted change order and it became apparent that the majority of the work had been done prior to the Public Works Department submitting the change order. The City's Public Works Director, Raj Verma, resigned shortly thereafter.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report

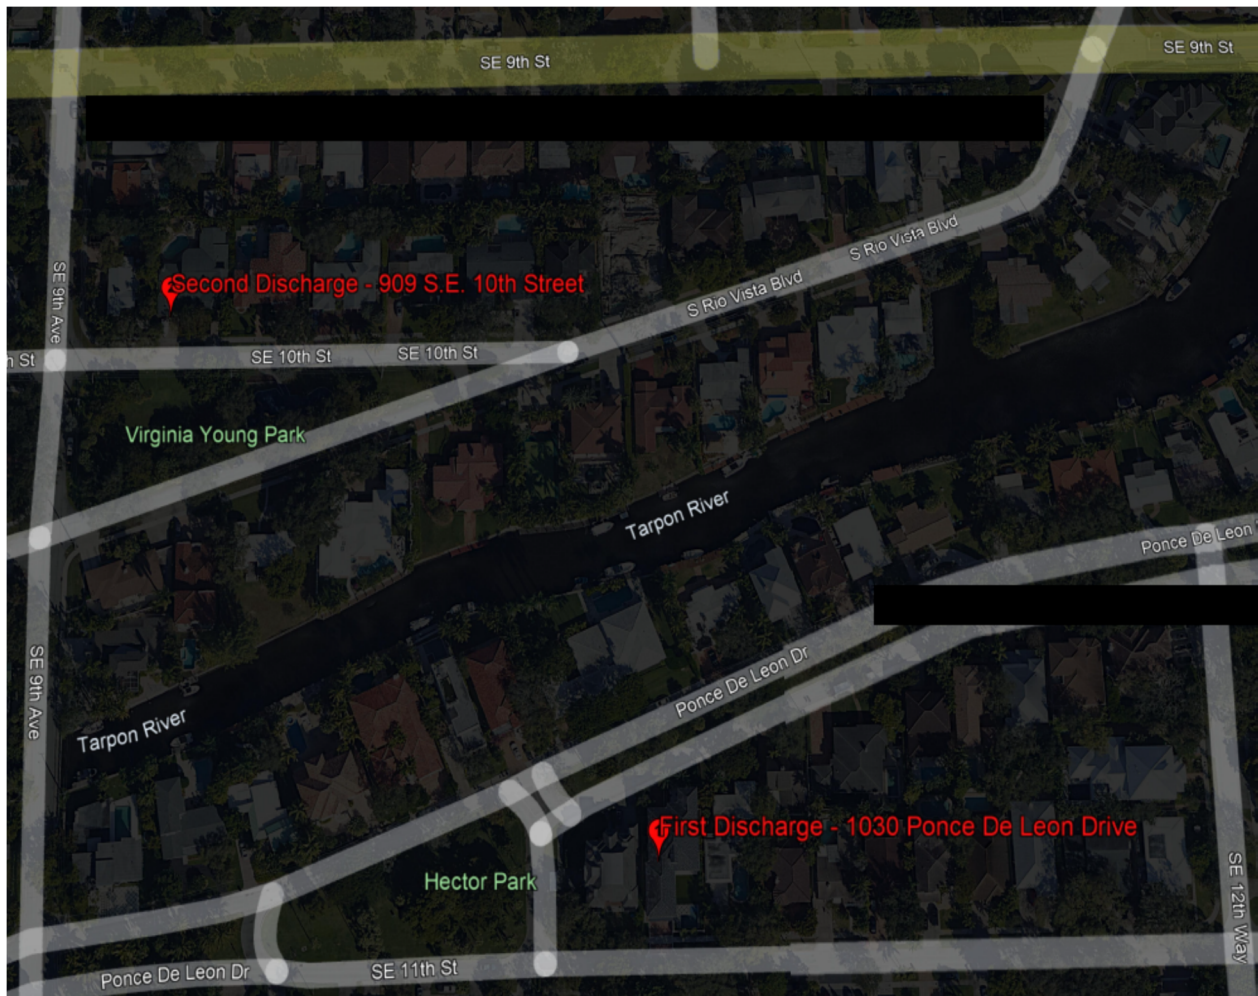

CRI's Forensic Team participated on a conference call with the City Auditor's Office on July 27, 2021. During this conference call, the City Auditor's Office expressed its concerns over the Rio Vista Restoration Project and whether or not City policies and procedures were followed or overridden. CRI was subsequently engaged on August 10, 2021 to provide the requested forensic accounting services for the City.

Scope

Our investigation was for the period beginning December 1, 2019 through August 31, 2021. Our work was limited to those specific areas identified by the City. As delineated in subsequent sections of this report, certain key individuals declined CRI's request for interviews. Relevant, known communications were reviewed in relation to these individuals. Based on the available information, CRI does not believe that interviews with these individuals would substantively affect the findings and conclusions in this report.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Approach

Our engagement was conducted in accordance with the Statement on Standards for Forensic Services No. 1 (SSFS) and applicable professional standards promulgated by the American Institute of Certified Public Accountants (AICPA). The AICPA's SSFS does not specifically require or promote the use of certain methodologies, techniques, etc. for forensic engagements. This is due to the fact that no single standard can be extensive enough to consider all of the potential methodologies, techniques, etc. that could be applied to every forensic engagement.

Rather, this statement implements general standards that should be followed during a forensic engagement. These standards include that an AICPA member should have the professional competence to perform the engagement and exercise due professional care during the performance of the engagement. These standards were followed during the course of our engagement.

Using the data provided to us, we performed the procedures enumerated in our engagement letter executed August 10, 2021 as delineated below. We also applied various commonly used forensic data mining techniques to the provided data to identify trends, patterns and potential internal control overrides in the data provided. These techniques and the identified trends/patterns/internal control overrides are outlined below.

Expert Qualifications

Ben Kincaid, CPA, CFE, CVA, CFF

Benjamin Kincaid has over 9 years of experience in public accounting and in providing a variety of forensic accounting services. These forensic accounting services include litigation support, financial fraud investigations, business valuations, lost profit calculations, etc. Mr. Kincaid has served as a consultant for several state, county and other local law enforcement agencies/governments and serves on the Florida Institute of Certified Public Accountant's Valuation, Forensic Accounting and Litigation Committee.

Additionally, Mr. Kincaid is a Certified Public Accountant, which is the premier designation in the accounting industry. The Certified Public Accountant license is regarded as a symbol that an accountant has mastered the vital elements of the accounting profession and is a high standard that is globally recognized as an assurance of skill, dedication and quality. Mr. Kincaid has also received the Certified Fraud Examiner and Certified in Financial Forensics designations. These forensic accountant designations are considered to be the most valuable forensic certifications. Holders of these forensic accountant designations are required to demonstrate a high level of knowledge and competence within the field of forensic accounting. Mr. Kincaid is also a Certified Valuation Analyst, which is the most widely recognized business valuation credential. A summary of Mr. Kincaid's résumé and qualifications is included in Appendix A of this report.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Rob Broline, CPA

Rob Broline has over 20 years of proven skills and experience in public accounting. Mr. Broline provides a variety of consulting and internal control services for governments, construction firms and other organizations. These services include entity-wide risk assessments, process risk/control assessments, internal audits, operational audits, construction cost audits and forensic reviews.

Mr. Broline is a Certified Public Accountant, which is the premier designation in the accounting industry. The Certified Public Accountant license is regarded as a symbol that an accountant has mastered the vital elements of the accounting profession and is a high standard that is globally recognized as an assurance of skill, dedication and quality. Mr. Broline speaks regularly on internal controls and related topics for a variety of construction and governmental organizations. A summary of Mr. Broline's résumé and qualifications is included in Appendix A of this report.

Steve Riggs, CPA, Cr.FA

Steve Riggs has extensive experience in public accounting and in providing a variety of consulting services. These consulting services include litigation support, forensic accounting, mergers and acquisitions, expert witness testimony, etc. Mr. Riggs has been qualified as an expert witness in several courts and has also served as a court appointed trustee. Mr. Riggs is a co-founder of Carr, Riggs & Ingram, LLC, which is one of the top 25 public accounting firms in the United States of America and was appointed to the Florida State Board of Accountancy.

Additionally, Mr. Riggs is a Certified Public Accountant, which is the premier designation in the accounting industry. The Certified Public Accountant license is regarded as a symbol that an accountant has mastered the vital elements of the accounting profession and is a high standard that is globally recognized as an assurance of skill, dedication and quality. Mr. Riggs has also received the Certified Forensic Accountant designation. The Certified Forensic Accountant designation is considered to be one of the most valuable forensic certifications. Holders of the Certified Forensic Accountant designation are required to be licensed Certified Public Accountants and must demonstrate a high level of knowledge and competence within the field of forensic accounting. A summary of Mr. Riggs' résumé and qualifications is included in Appendix A of this report.

Summary of Procedures Performed

1. Reviewed City policies and procedures related to the Rio Vista Restoration project.
2. Conducted interviews with the following individuals to obtain an understanding of the Rio Vista Restoration project, project approval process, project records and City policies and procedures:
 - a. Chris Lagerbloom, City Manager;
 - b. Ben Sorensen, City Commissioner;
 - c. Susan Grant, Finance Director;
 - d. Phil Thornburg, Parks & Recreation Director;
 - e. James Hemphill, Assistant Procurement & Contracts Manager;
 - f. Talal Abi-Karam, Assistant Public Works Director;

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

- g. Dr. Nancy Gassman; Assistant Public Works Director;
- h. Victor Carosi, Assistant Public Works Director;
- i. Omar Castellon, Chief Engineer;
- j. Rares Petrica, Senior Project Manager;
- k. Francisco Rios, Project Manager II;
- l. Elkin Diaz, Senior Project Manager;
- m. Kymberly Holcombe, Business Operations Manager;
- n. David Mancini, Jr., City Vendor; and,
- o. Fred Stresau, Rio Vista Civic Association Landscape Architect.

CRI requested to interview the following individuals, who declined to be interviewed.

- a. Raj Verma, former Public Works Director;
- b. Jodi Hart, former Procurement & Contracts Manager;
- c. Christina Currie, Rio Vista Civic Association President;
- d. Daniel Duke, Hinterland Group, Inc. President; and,
- e. Project Managers at Hinterland Group, Inc.

Hinterland Group, Inc. and Christina Currie declined the interviews through their legal counsel and/or referred us to their legal counsel. Ms. Hart stated she declined the interview as she did not recall anything specific regarding the Rio Vista Restoration Project. Mr. Verma declined due to various concerns regarding the audit.

- 3. Analyzed supporting documentation including certain City personnel's electronic data for the Rio Vista Restoration Project for compliance with the City's policies and procedures.
- 4. Determined whether the City's internal controls were overridden by City personnel and identified the individuals responsible for the internal control overrides.

Source Documentation

We reviewed and relied upon the documentation listed in Appendix B of this report during our investigation. These documents included, but were not limited to, contracts, purchase orders, electronic communications and payment applications.

Finding 1

Policies and Procedures

The City has adopted various ordinances as well as internal policies and procedures (herein collectively referred to as policies and procedures). These policies and procedures guide the operation of the City and help form the basis for the City's internal controls. We reviewed the City's policies and procedures applicable to the Rio Vista Restoration Project. This information as well as our interviews with City personnel provided us with an understanding of the City's policies and procedures. This understanding and specific policies and procedures are addressed further in subsequent sections of this report.

Finding 2

Understanding of the Rio Vista Restoration Project

The interviews provided us with an understanding of the Rio Vista Restoration Project, project approvals, project records and the City's policies and procedures. The interviews also provided us with an understanding of the individuals involved in the Rio Vista Restoration Project including City personnel and individuals not employed by the City.

The City adopts an annual Community Investment Plan (CIP), which reflects a 5-year capital project plan by funding source. The CIP provides direction to the responsible City departments/divisions on which capital projects are to be undertaken. As part of the adopted fiscal year 2019-2023 and 2020-2024 CIPs, funding from the City's Stormwater Fund was established for Hector Park Stormwater Improvements (Project No. P12020). The Engineering Division of the Public Works Department was responsible for the Hector Park Stormwater Improvements. Within the Engineering Division, there are designated teams for certain fund/project types; such as, stormwater projects. The stormwater improvement team (herein referred to as the stormwater team) is overseen by Omar Castellon, Chief Engineer. Mr. Castellon's team includes Rares Petrica, Senior Project Manager, and Francisco Rios, Project Manager II.

The stormwater team generally utilizes the stormwater construction contract for its capital projects. The stormwater construction contract was a continuing, master contract and was the result of a sealed bid solicitation in 2017. The four awarded vendors were Hinterland Group, Inc., Southeastern Engineering Contractors, Inc., DP Development of the Treasure Coast, LLC and G P E Engineering & General Contractor Corp.

Projects are assigned to these vendors utilizing task orders. Task orders are awarded to these vendors on a rotational basis. The rotation may vary depending upon a vendor's ability, specialty experience, previous task order amounts, ongoing City projects, etc. Per City staff, the task orders and cumulative task order amounts by vendor will vary due to these exceptions. Task orders are not pre-planned for certain vendors.

In or around September 2019, Task Order No. 15 was issued to Hinterland for the Hector Park Stormwater Improvements Project (Hector Project). City staff indicated that Hinterland was awarded this task order as part of its normal rotation process for the stormwater construction project. The Hector Project was scheduled to begin in December 2019. However, due to the sewer main break near Hector Park, the Hector Project was postponed. Mr. Castellon stated that Hinterland was not involved in the sewer main break emergency project (emergency project).

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Understanding – Project/Contractor Assignment

During the emergency project and the sewer main line replacement project, the City allowed its contractor, David Mancini & Sons, Inc., to utilize Hector Park as a staging area for quicker mobilization. The staging caused additional damage to the parks and delays in restoring the parks from the sewer breaks. In January through March 2020, the City had various meetings regarding the restoration of Hector Park and Virginia S. Young Park. In an early March 2020 meeting that included the City Manager, Chris Lagerbloom, it was determined that the Public Works Department would take the lead in the Rio Vista Restoration Project.

Per Dr. Nancy Gassman, Assistant Public Works Director, Mr. Verma stated that he would lead this project and appoint a project manager for the Rio Vista Restoration Project. In late March 2020, Mr. Verma assigned Francisco Rios, Project Manager II, as the project manager of the Rio Vista Restoration Project. Mr. Rios indicated that Mr. Verma’s rationale for assigning the stormwater team to this project was due to the stormwater team being “already in there” for the Hector Park Stormwater Improvements Project. Mr. Rios further indicated that Mr. Verma initially planned to utilize “in-house staff” for the Rio Vista Restoration Project with the potential support of David Mancini & Sons, Inc. This initial plan changed due to staffing resources/other project commitments within the Public Works Department.

In April 2020, Mr. Verma stated to the stormwater team including Public Works Business Operations Manager, Kymberly Holcombe, that he had discussed the Rio Vista Restoration Project with former Procurement & Contracts Manager/Chief Procurement Officer, Jodi Hart. Mr. Verma relayed that Ms. Hart had “signed off” on utilizing Hinterland under the stormwater construction contract for the restoration project. Mr. Castellon stated that Hinterland was chosen for this work since they were “already there.” In or around October 2020, Task Order 25 was issued to Hinterland for \$1,717,817 for the Rio Vista Restoration Project.

Mr. Rios stated that the Public Works Department did not prepare any design plans for the Rio Vista Restoration Project. Mr. Rios further stated that the Rio Vista Restoration Project involved “day by day design construction.” Mr. Rios indicated this was unusual as the planning process normally takes up to one year for the design and permitting that needs to occur before construction. When asked why the normal process was bypassed, Mr. Rios stated that it was Mr. Verma’s direction to get this project done and that the “City wanted [it] done ASAP.”

Understanding – Playground Restoration

City staff indicated that the parks were damaged during the emergency project. Fred Stresau, a certified Landscape Architect voluntarily working with the Rio Vista Civic Association, stated the playground equipment within the Virginia S. Young Park could have been cleaned with a pressure washer as the playground equipment was not that old. However, City staff indicated that various parts of the playground equipment were damaged and it was determined that the playground equipment needed to be replaced.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

The stormwater team worked with the Public Works Department's former in-house landscape architect, Thomas White, for the Rio Vista Restoration Project. Mr. Petrica stated that a project manager within the Parks & Recreation Division stated that she did not want to be involved in this project. Mr. Castellon stated that the stormwater team "does not do park restoration; it should be the Parks & Recreation [Department]." Phil Thornburg, Parks & Recreation Director, stated that he worked with Mr. White regarding the initial playground design, but he was not involved much after July 2020. Mr. Thornburg also stated that "he did not have a role [in the Rio Vista Restoration Project] and [he] was not asked to be involved [in it]."

Mr. Thornburg stated that the Rio Vista neighborhood was involved in the planning process for the park restorations. Mr. Thornburg indicated that this is not unusual as the City wants to provide for the neighborhood's needs/wants within the allotted amount of money for the parks. Commissioner Ben Sorensen (Commissioner Sorensen) affirmed this by stating that the City "put it up to the [Rio Vista] neighborhood as they know better what they want" and the City "let the [Rio Vista neighborhood] drive the park playground equipment process." Commissioner Sorensen stated that he did not have a role in the park design/equipment selection. In or around April 2020, the Rio Vista neighborhood approved playground equipment built by Kompan, Inc., a higher-end playground equipment manufacturer based in Denmark. Commissioner Sorensen stated that Kompan playground equipment is used all around the City. Mr. Thornburg stated that he believed that the Rio Vista neighborhood is the only park with Kompan playground equipment, but the Kompan playground equipment price was not exorbitant.

Mr. Thornburg stated that both the Virginia S. Young Park and Hector Park were planned for rehabilitation as part of a \$200 million parks bond issued in 2019. Due to the future rehabilitation, it "made sense to use [the] park bond money" for the parks restoration. Mr. Thornburg and the Rio Vista Civic Association made a presentation to the Parks, Recreation and Beaches Advisory Board regarding the use of the park bond monies for Hector Park and Virginia S. Young Park. The Advisory Board recommended approving the use of the park bond monies. In July 2020, the City Commission approved the Advisory Board's recommendation and the park designs. The City Manager stated that the parks/playground equipment costs were not provided to/approved by the City Commission.¹

Understanding – Additional Projects/Change Order

City staff indicated that Mr. White had estimated the cost of the playground at Virginia S. Young Park at \$200,000. The playground cost and related park restoration costs funded by park bond monies were included in the original Task Order 25 for \$1,717,817. Mr. Hemphill, Assistant Procurement & Contracts Manager, stated that the Procurement Services Division reviewed and approved Task Order 25. No issues were raised on Task Order 25 and Ms. Hart approved it per Mr. Hemphill. Mr. Hemphill stated that the Procurement Services Division is not an expert in construction and does not know what is occurring at each project. Instead, the Procurement Services Division relies on the information provided by the project manager.

¹ City Agenda Memorandums 20-0501 and 20-0092 included budget amendments/fund reallocations related to the Rio Vista Restoration Project. These budget amendments were approved by the City Commission. However, the budget amendments do not reflect the City Commission's approval of the costs and no detailed cost information was presented to the City Commission.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Ms. Holcombe stated that the original Task Order 25 was within the stormwater construction services contract cap and that there were no issues with the task order. Ms. Holcombe believed that all task order items aligned with the contract. Ms. Holcombe stated that Ms. Hart complied with City policies and procedures. Ms. Holcombe further stated that “the fact that Jodi [Ms. Hart] was comfortable with the task order things...that way my green light.” Ms. Holcombe stated that this was supported by Ms. Hart’s signature on Task Order 25 and Ms. Hart’s conversation with Mr. Verma.

As the Rio Vista Restoration Project progressed, various scope changes were added. Mr. Castellon stated that Hinterland was “doing the work with no approval.” Mr. Rios stated that he was told to “lump all items/changes into one CO [change order] because it takes too long.” Mr. Verma and the stormwater team provided this direction and/or were aware of this direction per Mr. Rios. Mr. Rios indicated that Mr. Verma had stated that “if they followed the change order process, the project would not get done.” Mr. Petrica described the change order options as “do a change order for each change or wait and lump them together at the end.” Mr. Petrica stated that Mr. Verma decided to choose the latter option. Mr. Rios stated that Hinterland agreed to this approach.

Mr. Petrica also stated that this project had “a lot of scope creep.” Mr. Petrica described the water main replacement, road raising, road narrowing, playground and lights as being scope creep on this project. As the project continued to progress, the scope creep continued. Mr. Rios indicated that Hinterland started to slow down its work on Rio Vista Restoration Project as Hinterland was not getting paid. Mr. Castellon stated that at one point Hinterland called and said they were not going to do any more work until they got paid. Mr. Rios indicated that he told Hinterland that they would get a change order approved for its additional work.

In or around May 2021, the Public Works Department started to prepare a change order to Task Order 25 related to the additional work/scope performed by Hinterland. Mr. Castellon indicated that Hinterland had performed 80%-90% of the additional work/scope by June 2021. Ms. Holcombe stated that she did not discuss the change order with anyone; however, Mr. Verma was pushing to get the change order done. Ms. Holcombe further stated that everyone in Public Works was addressing the change order with urgency. The change order for Task Order 25 was approved by the Procurement Services Division without any issues being raised.

Per Susan Grant, Finance Director, the Commission Agenda Memorandum for the change order to Task Order 25 came into her queue in June 2021. Ms. Grant started questioning the change order and had a discussion with Mr. Verma regarding the change order. Ms. Grant stated that it became apparent that the work had been done without a valid, approved change order in place. Mr. Verma subsequently sent Ms. Grant an e-mail regarding their discussion. Ms. Grant immediately informed the City Manager and the City Attorney regarding the change order. Ms. Grant related that the Procurement Services Division probably should not have approved the original Task Order 25 with the playground equipment cost included in it. Prior to Ms. Grant’s tenure with the City, the City Attorney reviewed every task order, but this became too onerous and it was later delegated to the Chief Procurement Officer, Ms. Hart. The City Manager stated that he was aware that the City was performing restoration work for the Rio Vista neighborhood, but he was not aware that the restoration work was going beyond the normal level of restoration.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Understanding – Procurement Process

Per the stormwater team, Mr. Verma hoped to have the Rio Vista Restoration Project change order approved as an emergency purchase. City staff interviewed uniformly agreed that the Rio Vista Restoration Project was not an emergency and did not qualify as such under the City's Procurement Manual.

As previously indicated, task orders are utilized for continuing, master contracts. Initially, a purchase requisition is entered for each awarded vendor for an equal amount of the contract award amount. The purchase requisition can be adjusted up or down based on task orders and available funding. City staff indicated that they can issue an initial task order up to the available funds/contract award amount/cap without additional City Commission approval. City staff indicated that there are no contract amounts with each vendor, only the total contract award amount on the master contract.

City staff indicated that any change order or cumulative change orders in excess of 10% of the original amount require City Commission approval. There was some confusion among City staff whether the 10% related to the contract amount or the task order amount. Ms. Grant stated that the Procurement Manual is not clear on this issue. However, it should be based on the task orders based on historical interpretation by Ms. Hart, the former Chief Procurement Officer. Change orders that fall below the 10% threshold may be approved by the Chief Procurement Officer. Ms. Holcombe stated that change orders to task orders are generally for unforeseen project conditions. A small portion of Public Works' change orders exceed 10% of the initial task order.

The stormwater construction services contract was a line item contract, where City vendors agree to set rates for certain types of goods and services. Per the stormwater team, they try to be as broad as possible in the line item contracts, as they never know what type of unforeseen circumstances/goods/services may be required for certain stormwater capital improvements. As a result, the stormwater construction services contract includes various pass-through item allowances. These pass-through line item allowances include specialized construction services and landscaping allowances. Mr. Petrica indicated that the line items/allowances utilized by the stormwater team for Task Order 25 made sense with the project scope's actual design. Mr. Hemphill stated that Task Order 25 listed playground along with testing under the specialized construction services pass-through line item. This listing did not raise an issue at the time when Ms. Hart approved it according to Mr. Hemphill.

Understanding – City Commissioner Involvement

The City Manager, Chris Lagerbloom, stated that City Commissioners may make inquiries with City staff, but they cannot provide directives to City staff/vendors. The City does not provide specific training for commissioners regarding their interaction with City staff. However, the City Attorney does provide guidance to commissioners regarding their interaction with City staff. City staff indicated that no training or policies and procedures are provided to them regarding interactions with City Commissioners. The City Manager stated that he does not want to be the one to stop/hold up progress on City operations. The City Manager requests that City staff keep him in the loop, but that he likes them to handle commission inquiries like they were him to a certain degree. Mr. Lagerbloom stated that Commissioners may interact with Department Directors and maybe Assistant Department Directors, but no one below the Assistant Department Director level. Mr.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Lagerbloom also stated that it is okay for Commissioners to ask vendors questions “here or there,” but they should not give direction to the vendors.

Commissioner Sorensen stated that he viewed his role as Commissioner as being an advocate for people and brought matters/concerns to City staff. Commissioner Sorensen stated that there is no formal onboarding process for Commissioners, but he knows the ethics requirements as there is ethics training provided by the City.² Commissioner Sorensen stated that “Commissioners cannot direct staff. Commissioners cannot direct contractors.” Commissioner Sorensen further stated that he “cannot say ‘fix that’”; instead, that type of request must be sent to the City Manager.

Commissioner Sorensen stated that he lives in the Rio Vista neighborhood and that the sewer breaks were a big issue in the City. Commissioner Sorensen was described as full of energy and committed to his district. Commissioner Sorensen was also described as being more engaged on the Rio Vista sewer breaks. The City Manager stated that the City’s sanitation division brought to his attention during the emergency project that Commissioner Sorensen was getting too involved in the emergency project. One of the examples provided related to Commissioner Sorensen interacting/driving around with one of the City’s vendors, Cliff Berry, Inc., during the emergency project. Separately, one City staff stated to us that Commissioner Sorensen “direct[ed] the sewage cleanup.” Mr. Lagerbloom stated that he had a private discussion with Commissioner Sorensen regarding this issue. Commissioner Sorensen stated that he may have had a discussion with the City Manager regarding it, but he could not recall.

Commissioner Sorensen stated that he talked to the Public Works Department staff “pretty regularly.” Commissioner Sorensen further stated that he would meet with someone from Public Works every few weeks and would be in touch with them regularly. Commissioner Sorensen reiterated that his correspondence with Public Works were “inquiries only; just questions.” Commissioner Sorensen indicated that he had no idea regarding the level of communication frequency with City staff, but that it would occur via phone calls, texts, e-mails and in-person.

Mr. Rios, the project manager, indicated that some weeks Commissioner Sorensen would contact him every day and other weeks at least 2 or 3 times per week. This occurred via phone calls, text messages, e-mails and onsite visits. Mr. Verma would also forward e-mails from Commissioner Sorensen to Mr. Rios for him to reply. Mr. Rios confirmed that this was an “unusual” level of involvement. Mr. Petrica noted that Commissioner Sorensen was on the project site “all the time” and that the project was Commissioner Sorensen driven. Mr. Castellon stated that the stormwater team knew that the City Charter prohibits Commissioners from giving direction to staff. Mr. Castellon stated that Commissioner Sorensen did not give him any direction, but he was uncomfortable with the direct communication with Commissioner Sorensen. Commissioner Sorensen would ask for a status update from Mr. Castellon throughout the Rio Vista Restoration Project. Although this was an inquiry from Commissioner Sorensen, Mr. Castellon took it as “get it done.”

² In March 2019 and June 2021, the City Attorney communicated to City Commissioners reminders regarding the City Charter prohibiting “the City Commission from giving direction or orders to City staff” and that “any direction or order for [City] staff to act, except for purposes of obtaining and providing information, should be directed through the City Manager.”

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Mr. Rios noted that Commissioner Sorensen would call about specific items/questions, but the calls would also involve status updates. Mr. Rios stated that he did not receive specific direction from Commissioner Sorensen (i.e., “go fix this”). Instead, Commissioner Sorensen would ask “Can you fix this?” or “Is this something we can do?” Mr. Rios stated that his impression was that it needed to be done and he felt pressure to do so. In response to a later direct question regarding if anyone directly or indirectly pressured him, Mr. Rios subsequently stated that he was “unsure” if Commissioner Sorensen pressured him. Mr. Rios stated that the pressure came from his boss, Mr. Petrica, Mr. Castellon and Mr. Verma. Mr. Rios also stated that Commissioner Sorensen requested that they [Public Works/Hinterland] add additional staffing to the Rio Vista Restoration Project.

Mr. Castellon stated that Public Works had many meetings with the neighborhood residents, Commissioner Sorensen and Mr. Verma. Mr. Castellon further stated that there “was a lot of pushback from [Commissioner] Sorensen and the [neighborhood] residents to [Public Works].” Mr. Rios stated that Commissioner Sorensen met with the Rio Vista neighbors, who provided a lot of feedback to him. Commissioner Sorensen, along with a Rio Vista neighborhood resident, requested that Mr. Castellon “get rid of Hinterland and [to] not give [any] more work” to Hinterland in or around June 2021. Mr. Castellon stated that they could not get rid of Hinterland at that point.

Mr. Rios also stated that the Rio Vista neighborhood wanted their neighborhood better than what it was prior to the sewer breaks. Mr. Rios stated that “no one would tell them [Rio Vista neighborhood] no. Raise the road? Yes. Narrow the road? Yes. Add ramps? Yes. Buy park equipment? Yes.” Public Works “did what [Commissioner] Sorensen wanted them to do.” Mr. Castellon stated that there was one meeting where Commissioner Sorensen and certain Rio Vista neighborhood residents approached the Public Works team onsite, which consisted of Mr. Castellon, Mr. Verma, Mr. Petrica and Mr. Rios. Mr. Verma met with the residents and Commissioner Sorensen. Mr. Petrica and Mr. Rios both recalled this meeting as well. After Mr. Verma concluded the meeting, Mr. Verma added to the project scope. Mr. Castellon stated that it was Mr. Verma’s decision to add to the project scope, but he observed agreement between Mr. Verma and Commissioner Sorensen.

The stormwater team did not observe interactions/meetings between Commissioner Sorensen and Hinterland, the project vendor. Mr. Rios noted that around April 2021, Hinterland’s president, Daniel Duke, relayed to Mr. Rios that Commissioner Sorensen purportedly communicated with Hinterland. Mr. Rios stated that he had “never seen it happen before” where a Commissioner interacted with a vendor. Other City staff indicated that it does happen where a Commissioner interacts with a vendor, but that it is unusual.

Commissioner Sorensen stated that he “never directed [City] staff/[vendors]” on the Rio Vista Restoration Project. Commissioner Sorensen stated that he in “no way” directed City staff to bypass City policies and procedures. Commissioner Sorensen did not have any concerns regarding the project scope/approval as Public Works said they could do it. Commissioner Sorensen further stated that he never pressured City staff/vendors to do anything. Commissioner Sorensen was asked whether given the volume of his correspondence to City staff if City staff could have felt pressured

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

by it. Commissioner Sorensen responded “maybe – [I] cannot get in their minds.” Commissioner Sorensen, in response to a separate question regarding City staff direction/pressure, stated that strongly pressuring/directing City staff was “not needed; not allowed. [City] staff put pressure on themselves.” Commissioner Sorensen also stated that in retrospect, the City Manager or Assistant City Manager should have been included in the communications.

Commissioner Sorensen stated that he did have contact with City vendors. When asked what those contacts involved, Commissioner Sorensen stated that these contacts occurred at neighborhood civic association meetings or where he inquired regarding project updates. Commissioner Sorensen recalled that Hinterland did relay that they were having a tough time getting in touch with City staff regarding getting paid and he relayed the information back and forth between Hinterland and Public Works.

Understanding – Public Works Director Overrides

City staff stated the former Public Works Director, Raj Verma, was a hands-on manager. Mr. Verma was also described as having a plan to change the entire Public Works Department. City staff indicated that Mr. Verma had a desire to get the work done. City staff almost uniformly stated that Mr. Verma would say “just get it done” in response to project questions.


City staff also stated repeatedly that Mr. Verma expressed frustration about the process to get things done and that policies have to change. Mr. Lagerbloom stated that Mr. Verma was dismissive of policies and procedures and believed that following policies and procedures slowed things down. Dr. Gassman stated that Mr. Verma was “cavalier and had a general attitude to just get work done and disregard policies and procedures if they get in the way.” Commissioner Sorensen also noted that Mr. Verma expressed frustration with City policies and procedures.

Mr. Castellon stated that he received an e-mail from Mr. Verma directing him to bypass City policies and procedures.³ Dr. Gassman stated that Mr. Verma “instructed staff to work outside of policies and procedures of the City.” The stormwater team stated that they all questioned Mr. Verma’s direction for scope additions and bypassing policies and procedures. Mr. Verma would reply that the “park went through a lot” so the stormwater team “went above and beyond” for the Rio Vista neighborhood. The stormwater team also stated that there were various internal discussions complaining about all of the changes and the volume of communications from Commissioner Sorensen and the Rio Vista neighborhood residents. Mr. Rios stated that they [the stormwater team] were instructed to handle it by Mr. Verma. Mr. Rios stated that he “felt [Mr. Verma] should have told Commissioner Sorensen no, but he did not. Eventually they [stormwater team] just did what he [Commissioner Sorensen] wanted them to do.” Mr. Castellon described it as Mr. Verma did not provide any other options – “Commissioner Sorensen pushed this.” Dr. Gassman described it as “Commissioner Sorensen wants X, make this happen.” Dr. Gassman stated that Commissioner Sorensen did not pressure her; instead, Mr. Verma raised the priority on staff to respond. Mr. Petrica described to us the apparent approval hierarchy was the Rio Vista neighborhood,

³ It appears Mr. Castellon was referring to a June 2021 “after the fact” e-mail from Mr. Verma.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Commissioner Sorensen and then Mr. Verma. A summary of the described approval hierarchy versus the appropriate approval hierarchy is presented in the below flow chart.

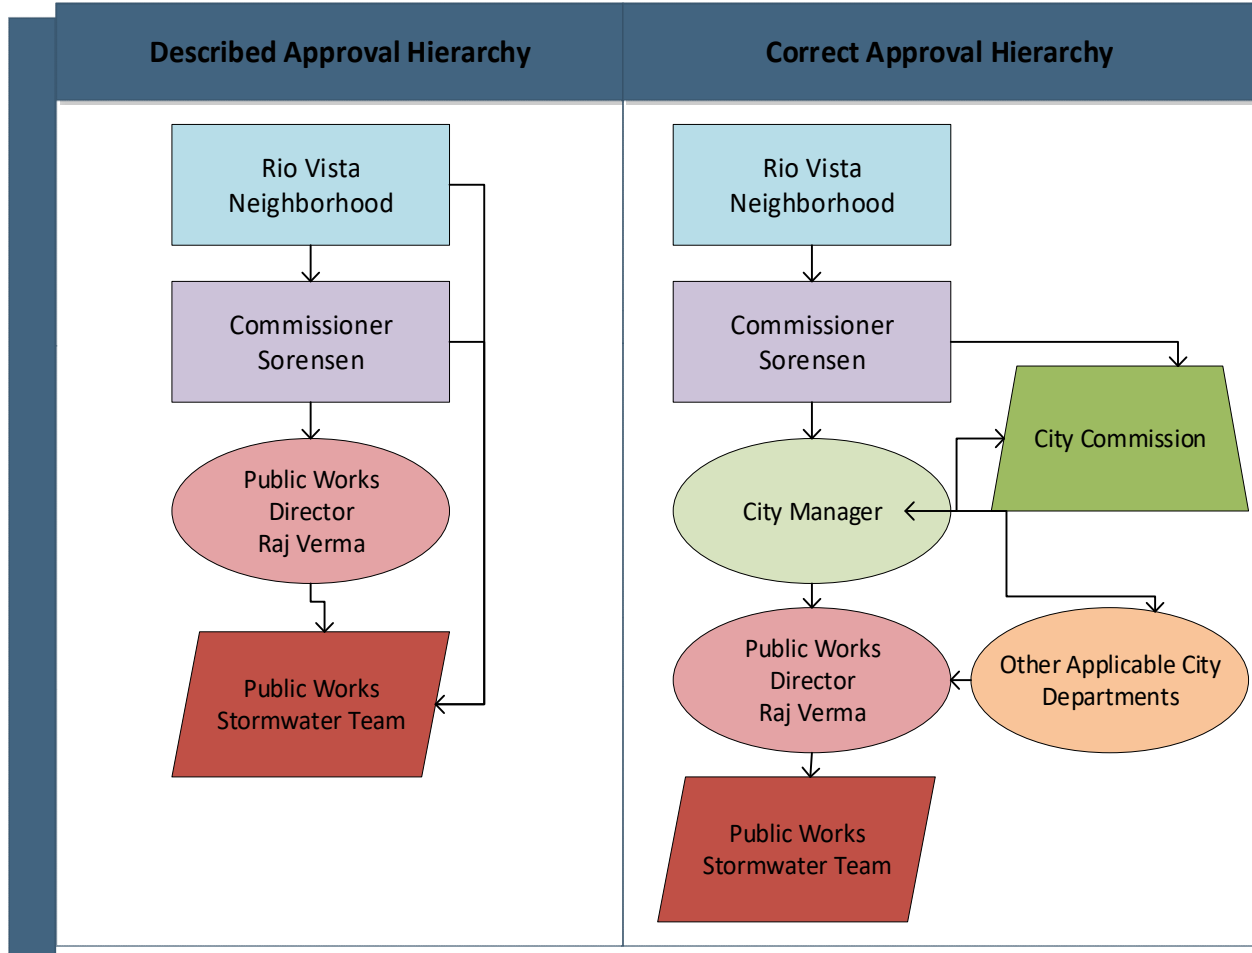

Mr. Lagerbloom stated that he was unaware that Mr. Verma had bypassed City policies and procedures until the City Finance Director, Susan Grant, brought it to his attention in June 2021. Mr. Lagerbloom referenced an e-mail from Mr. Verma in June 2021 in which Mr. Verma stated that following City policies and procedures and doing the work became impossible. Mr. Lagerbloom also stated that he was unaware of Commissioner Sorensen’s purported involvement in the Rio Vista Restoration Project and unaware that Mr. Verma could not “rein in citizens and Commissioner Sorensen.” Mr. Verma did not inform him of these issues. Mr. Lagerbloom indicated that he knew the Rio Vista neighborhood was energized and involved in the community, but that it was nothing new. Mr. Lagerbloom stated that he questioned Mr. Verma regarding these issues in June 2021. Per Mr. Lagerbloom, Mr. Verma was dismissive of his questions and said “Well Chris, you know how the Commissioners are...” Per Mr. Lagerbloom, he told Mr. Verma that their “job is to push back when needed” and Mr. Verma replied that “you know how this goes.”

Finding 3

Supporting Documentation Analysis – Renewal/Change Order Interpretations

The City's procurement ordinance requires that the City Commission approve contracts equal to or greater than \$100,000. In June 2017, the City Commission (CAM 17-0642) approved the contract award for the stormwater construction services contract in the estimated aggregate amount of \$4,500,000. The City Commission also authorized the Chief Procurement Officer, as the City Manager's designee, to approve two, one-year renewal options contingent upon fund appropriation.

In May 2018, the City Commission (CAM 18-0423) approved an award increase to the stormwater construction services contract of \$2,000,000. This was due to the use of the stormwater construction services contract by other departments and the original award of \$4,500,000 being exceeded after the first contract year. The Chief Procurement Officer administratively renewed the stormwater construction services contract in 2019 and 2020. In the administrative renewals, the Chief Procurement Officer also approved renewal contract award increases totaling \$6,500,000 (\$4,500,000 contract award + \$2,000,000 contract increase) for 2019 and 2020. The renewal contract award increases were not directly approved by the City Commission.

The stormwater construction services contract does not have an award amount listed due to it being a line item/unit price contract. The stormwater construction services contract provides that "any increase to the contract price shall be executed through an amendment to [the] agreement and approved by the City Commission." It further provides that "should the cumulative amount of the executed task orders exceed the contract price, a contract amendment must be approved by the City Commission authorizing additional funding for this contract."

Per the City's Procurement Ordinance and Procurement Manual, the Chief Procurement Officer is authorized to issue change orders increasing a contract price awarded by the City Commission up to 10% cumulatively. If the cumulative change orders exceed 10% of the contract price awarded by the City Commission, the change order must be approved by the City Commission. As previously indicated, the City has historically interpreted that the 10% change order threshold is based on task orders not the contract. This interpretation does not appear to align with the City's procurement policies and procedures. The City's Procurement Manual only addresses continuing contracts and task orders under Architectural and Engineering Professional Services Solicitations, which would not apply to the stormwater construction services contract.

Supporting Documentation Analysis – Contract Interpretation

As previously indicated, the stormwater construction services contract was utilized for the Rio Vista Restoration Project. The use of the stormwater construction services contract for this project was approved by Mr. Verma and Ms. Hart. The stormwater construction services contract, as its name implies, was intended only for stormwater capital improvement projects. This is supported by the contract, the bid solicitation and the Commission Agenda Memorandum.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

For example, Bid Item # 377 under the stormwater construction services contract was a pass-through cost item for specialized construction activities. The description for this bid item included full compensation for miscellaneous labor and equipment needed during construction, which was not specifically covered by other bid items in the contract. The Public Works Department and the Procurement Services Division interpreted that, based on the bid item description, the Virginia S. Young Park playground equipment was specialized construction activity. This is supported by the below e-mail excerpts.

June 14, 2021: Mr. Verma to various City personnel including Mr. Hemphill, Penelope Burger, Rhonda Hasan, Ms. Grant, Glynis Burney and Alain Boileau
“According to the PW PMs [Public Works Project Managers], although it is theoretically a ‘stormwater’ contract, there are many other allowable items.”

September 1, 2020: Ms. Hart to Mr. Petrica and other City personnel including Mr. Verma and Mr. Hemphill

“A Prime or Sub can only be used for the scope covered in the contract. If the contract for structural bridge consulting services does not include a scope that would be applicable for the [seawall] work we need, then it doesn’t matter if the contractor is capable to do the work we want. The scope of the contract needs to align to the scope of the work.

I am not a Subject Matter Expert to know what contracts we have that would cover the seawall work that you would like performed. If the scope of the annual civil consultants contracts includes seawalls, then having this vendor as a sub of an awarded Prime would be a way of accomplishing [the] contracting.”⁴


It does not appear that the line item scope interpretation was limited to the Rio Vista Restoration Project. In September 2017, the City Commission (CAM 17-0889) approved an award increase to the stormwater construction services contract for DP Development of the Treasure Coast, LLC. Per the Commission Agenda Memorandum, the award increase related to construction services at the Fort Lauderdale Executive Airport. Specifically, the outlined scope of work for this project included milling and resurfacing two inches of runway asphalt and leveling the new runway asphalt surface. The scope of work for this project does not appear to be stormwater related based on the available information. Interviews and e-mail correspondence with/by Mr. Hemphill and Ms. Grant confirmed that these broad and/or conflicting interpretations were not limited to the Rio Vista Restoration Project.

⁴ It should be noted that based on the available correspondence, it appears that here the Public Works Department and Procurement Services Division were reviewing the contract line items not the overall contract scope.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report

Supporting Documentation Analysis – Additional Scope

The Rio Vista Restoration Project’s scope changed continually throughout the review period. A timeline of the project and the project scope changes are presented below.

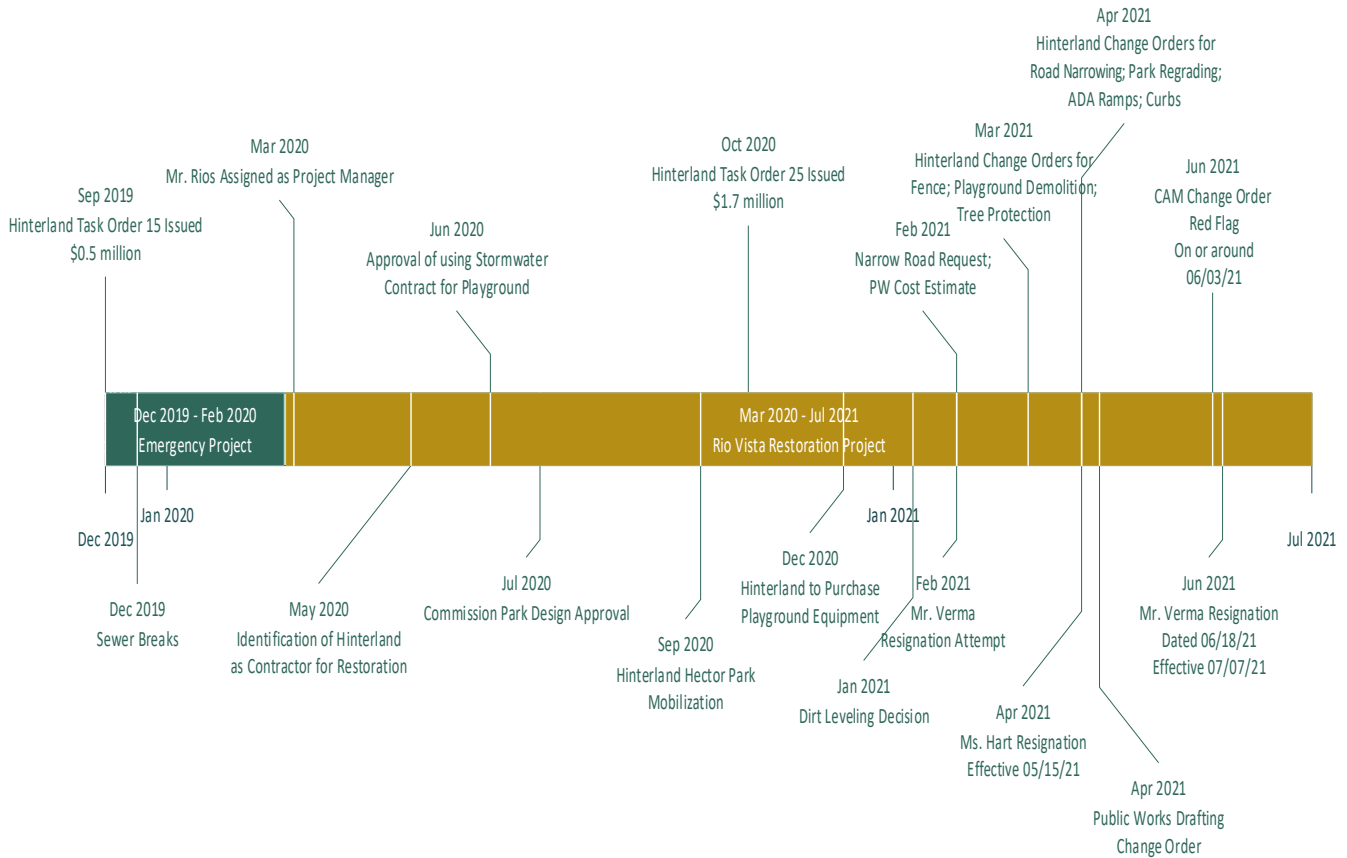

As outlined above, the original task order (Task Order 25) for the Rio Vista Restoration Project was issued in October 2020. The task order was approved by various staff levels in the Public Works Department and the Procurement Services Division. Approvers included Mr. Rios, Mr. Castellon, Ms. Holcombe, Shannon Barrett, Maria Santiago, Kimberly Smith, Aneisha Daniel, Mr. Hemphill and Ms. Hart. Task Order 25 project scope included parks restoration, water main replacement, water services, asphalt paving, curb, sidewalk and landscape restoration. The total task order amount was \$1,717,817.

In July 2020, the City Commission (CAM 20-0501) approved the Parks, Recreation and Beaches Advisory Board’s Recommendation to utilize a portion of the City’s \$200 million general obligation bonds for rehabilitating Hector Park and Virginia S. Young Park. The City Commission approved the park designs but did not approve any costs. Virginia S. Young Park was allocated \$331,500 in park bond monies for new playground equipment including shade tents and lighting, parallel parking, picnic tables, benches, new sod, etc. Hector Park was allocated \$74,500 in park bond monies for new trees, picnic tables, benches, new sod and a new irrigation system.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Task Order 25 was ultimately funded by three separate funds. These funds included roadway (\$884,440), central region water/sewer fund (\$439,337) and the park bonds [\$394,040 (Hector - \$72,307; Virginia S. Young - \$321,733)]. It appears that the Public Works Department knew that Task Order 25 did not have sufficient funds allocated to it prior to the issuance of the task order. This is supported by the below e-mail excerpts.

October 28, 2020: Relevant portion of e-mail series between Mr. Verma and Mr. Rios with other Public Works personnel copied.

FR: "My understanding is that we would need additional funds from Parks to make up the difference. I'm waiting on Hinterland to summarize the additional funds that we need, most of it is due to the playground cost, which was initially estimated at \$200,000, but they also had to add the cost of the tree protection, arborist, and the safety fence. The total additional cost is probably going to be around \$230,000 to \$250,000. If you don't have any objections, we can reach out to Enrique/Phil [Parks & Recreation] to request the additional funds once we have the actual amount from Hinterland."

RV: "Are these expenses over and beyond the original estimate?"

FR: "We have already used/encumbered \$394,040 for the parks portion on the executed task order [Task Order 25], which doesn't include the costs I mentioned below [above]."

This is in part due to the Public Works Department not properly planning for this project and prioritizing getting the project done. This is supported by a June 2020 e-mail from Mr. Verma stating that the Public Works Department would undertake the playground equipment demolition in-house. The Public Works Department ultimately requested that Hinterland perform the playground equipment demolition work, which was not planned for in Task Order 25. The task order also allotted only \$200,000 for the playground equipment replacement at Virginia S. Young Park, based on initial estimates prepared by Mr. White. The Public Works Department switched back and forth between the City purchasing the playground equipment and Hinterland purchasing the playground equipment. Ultimately, the stormwater team requested that Hinterland purchase the playground equipment. The order estimate for the playground equipment obtained by Hinterland in January 2021 totaled \$402,970.51, which is more than double the City's initial estimate. By having Hinterland purchase the playground equipment, sales tax totaling \$19,167.37 was assessed on the playground equipment and included in the Hinterland order estimate.

Based on the supporting documentation analyzed and interviews with City personnel, the Public Works Department requested that Hinterland perform additional scope/work not outlined in Task Order 25. The additional scope/work included fencing, park regrading, demolition of playground equipment, tree protection, road narrowing, raising of a road, watermain valves, temporary asphalt, lights, parking spaces, curbing and ADA ramps. As previously delineated in this report, Mr. Verma directed the stormwater team to wait on preparing a change order until the end of the project. Mr. Rios noted that Hinterland agreed to this approach.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

It should be noted that Hinterland submitted several change orders during early 2021 to Mr. Rios regarding these scope changes. Hinterland also requested confirmations from the stormwater team that the scope changes were approved. This is supported by the below e-mail excerpts.

April 23, 2021: E-mail series between Mr. Rios and Hinterland (Nelson Bello and other Hinterland personnel)

NB: "Per our field meeting this morning, we will be milling 1.5" on S Rio Vista Blvd and SE 10th Street as per the marked area on the attachment and paving two ¾" lifts. We will be issuing a change order for the proposed work. Please confirm that we [are] authorized to continue as discussed."

FR: "Please proceed."

May 5, 2021: Mr. Rios to Hinterland (Charles Emering, Daniel Duke, Chase Rogers, Jay Breig and Nelson Bello)

FR: "I agree that the Hector Park grading/berms, is new scope of work."

In or around April 2021, the Public Works Department started preparing a change order for the Rio Vista Restoration Project/Task Order 25. The change order went through numerous internal revisions. These revisions included increased change order amounts and language describing the change order. In its final, unapproved version, the change order totaled \$871,486.50, which increased the Rio Vista Restoration Project cost to \$2,589,303.50.

A large portion of the change order values were labeled as pass-through line items/allowances with minimal descriptions. Specifically, item number 377 totaled \$323,630. Per the supporting information, this pass-through line item/allowance included amounts/charges for an engineering firm, overtime/weekend charges and expediting fees. The stormwater team with Mr. Verma's approval agreed to these charges. However, several of these items were not eligible line items under the stormwater construction services contract.

It should be reiterated that the City did not approve this change order. The City made various payments to Hinterland for the Hector Project (Task Order 15) and the Rio Vista Restoration Project (Task Order 25). These payments totaled \$527,020.00 and \$1,527,525.90 for Task Order 15 and Task Order 25, respectively.

Supporting Documentation Analysis – Communications/Approvals

CRI analyzed various forms of electronic data related to certain City personnel involved in the Rio Vista Restoration Project. This included, but was not limited to, e-mails, Microsoft Teams messages, text messages and phone records. CRI noted that certain City personnel receive cell phone allowances from the City and utilize their personal cell phone for City business. CRI also noted that Commissioner Sorensen routinely utilized his personal cell phone for City business even though he is issued a City cell phone. Commissioner Sorensen offered for CRI to forensically examine his personal cell phone and retrieve City related data. This was ultimately not considered necessary based on our interviews with City personnel and other data obtained during our investigation. Commissioner Sorensen later provided various correspondence from his personal cell phone/e-mail that he identified during his review of his communications.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report

The correspondence provided by Commissioner Sorensen from his personal cell phone included correspondence related to City business. The correspondence included text messages, e-mails and WhatsApp messages. These communications were not provided by the City in relation to our document requests and the City was unaware of the existence of these communications. It is unknown/unclear whether all City related communications on Commissioner Sorensen’s personal cell phone were retained for public records retention purposes.

CRI identified numerous, frequent communications between the stormwater team including Mr. Verma and Commissioner Sorensen as well as Rio Vista residents. The level and frequency of communication supports the statements previously delineated in this report made by the stormwater team during their respective interviews. A summary of the available phone call records (December 2020 through August 2021) between applicable Public Works Department personnel and Commissioner Sorensen is presented in the below table.

City Employee	Desk Phones	Cell Phones	Total
Marie Pierce, Stormwater Operations Manager	2	-	2
Dr. Nancy Gassman, Assistant Public Works Director	1	-	1
Talal Abi-Karam, Assistant Public Works Director	-	-	-
Fransisco Rios, Project Manager II	5	35	40
Daniel Duke, Hinterland	-	2	2
David Mancini, Jr.	-	6	6
Elkin Diaz, Senior Project Manager	-	4	4
Raj Verma, Former Public Works Director	-	32	32
Victor Carosi, Assistant Public Works Director	-	1	1
Rares Petrica, Senior Project Manager	7	15	22
Omar Castellon, Chief Engineer	2	9	11
Total Calls	17	104	121

CRI identified numerous e-mail messages from Commissioner Sorensen to certain Public Works Department personnel during the review period. A large portion of Commissioner Sorensen’s e-mails to the relevant Public Works Department personnel were phrased in the form of a question. These e-mails included where Commissioner Sorensen forwarded communications from Rio Vista residents to the stormwater team and requested that the stormwater team address the Rio Vista resident’s questions/issues. A high-level summary of relevant e-mail communications between Commissioner Sorensen and the stormwater team are presented in Schedule A of this report. It should be noted that these e-mail communications were voluminous and this schedule presents only a sample of the communications.

During our interview with Commissioner Sorensen, Commissioner Sorensen was provided copies of certain e-mails referenced in this report. Commissioner Sorensen was inquired regarding how he viewed these communications and whether the communications arose to the level of directing City staff. Commissioner Sorensen reviewed these selected e-mails and stated that he was asking questions of City staff. He stated that maybe there is a grey area between inquiry and direction, but

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

his intention was inquiry. As previously indicated, Commissioner Sorensen stated that he never pressured City staff/vendors to do anything. Commissioner Sorensen was asked whether given the volume of his correspondence to City staff if City staff could have felt pressured by it. Commissioner Sorensen responded “maybe – [I] cannot get in their minds.” Commissioner Sorensen in response to a separate question regarding City staff direction/pressure stated that strongly pressuring/directing City staff was “not needed; not allowed. [City] staff put pressure on themselves.”

Based on our interviews with the stormwater team, the stormwater team believed that Commissioner Sorensen’s “inquiries” were implied directives, even though they were phrased in the form of a question. The below e-mail excerpt is an example of how City personnel interpreted Commissioner Sorensen’s “inquiries.”

June 3, 2021: Commissioner Sorensen to Residents, Mr. Petrica, Sayd Hussain, Mr. Verma, Mr. Rogers and Jill Prizlee.

Commissioner: “Yes, we will work on this. Rares, Sayd and Team, Can we have SE 2nd Court fixed/repaved?”

Ms. Prizlee: “FYI. 1)Alleyway; 2)Directive from Commissioner”

Various e-mails from Commissioner Sorensen to the stormwater team appear to be providing specific direction to the stormwater team. These e-mails include, but are not limited to, the following e-mails (the e-mails are summarized more fully on Schedule A of this report).

- June 17, 2020 – “Can we remove this boom?”
- January 7, 2021 – “When can the dirt be leveled?”
- January 16, 2021 – “Francisco will make sure this can work.”
- April 23, 2021 – “I would like it to be an individual choice for each homeowner. Can you confirm?”

There were also various e-mails and text messages from Commissioner Sorensen reflecting that Commissioner Sorensen provided direction to City vendors. Excerpts from these communications are presented below.

- November 30, 2020: Commissioner Sorensen to David Mancini, Jr. – “There are detour signs on the SE corner of Federal Highway and SE 7 Street. Can you remove those?”⁵
- January 14, 2021: Commissioner Sorensen to Rio Vista Residents and the stormwater team – “I was at Hector Park yesterday meeting with Jimmy with Hinterland...I would like the water main and the stormwater pipe done at the same time but we are waiting on further engineering work for the stormwater pipe...I will have the contractor [Hinterland] move them [excavated materials] further away from the fence so the material doesn’t spill over onto the roadway.”

⁵ Commissioner Sorensen was shown this text message during his interview. Commissioner Sorensen stated his intention was asking the vendor a question as he didn’t know whether or not the signs were the contractor’s or someone else’s.

**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

In October 2020, Commissioner Sorensen from his personal cell phone texted the City Manager regarding a fine issued by the City to Hinterland. The relevant text message excerpts are presented below.

October 25, 2020: Commissioner Sorensen to Chris Lagerbloom

CS: "Hinterland is the contractor doing work at Hector Park in Rio Vista. They got fined by the City. Can we forgive that fine? They feel they were allowed to dewater the way they were doing. The court case or something is tomorrow."

CL: "Will address tomorrow. They should not be contacting you. That is a huge problem - maybe unethical. Don't get yourself in a pickle. Send them to public works. It's a cutthroat business and Johnson would love to know Hinterland is contacting you directly. Just want you to protect yourself. I'm consistently getting nasty letters from that industry on who we call, who we call first, who we call second and why we chose one versus another."

CS: "Got it. Thanks"

It should be noted that Commissioner Sorensen communicated with Daniel Duke, president/owner of Hinterland, regarding payments from the City and the unapproved change order in the months following the above exchange. In a series of text messages provided by Hinterland, Commissioner Sorensen texted Mr. Duke that "it [Task Order 25 change order] is approved. I get 10 questions a day about the parks so the more info I have the better."

Many of the scope changes for the Rio Vista Restoration Project were generated by requests from the Rio Vista neighborhood. These requests were generally routed to Commissioner Sorensen, who elevated the requests to the stormwater team and Mr. Verma. As aforementioned, the stormwater team indicated that the residents and Commissioner Sorensen were pressuring the stormwater team and Mr. Verma regarding the Rio Vista Restoration Project. In an April 2021 e-mail, Mr. Verma stated that they were "under [a] lot of pressure to get this project completed." Based on the available information, Mr. Verma acquiesced to these requests and directed the stormwater team to add the requested additional scope items to the project. This is supported by the following e-mail excerpts:

February 21, 2021: Series of e-mails between Mr. Verma and Commissioner Sorensen as well as the stormwater team and Rio Vista residents.

CS: "We have alignment among the impacted neighbors - that they do not want parking spaces at the park. Raj, Rares and Francisco, Sorry for this change. Can you remove the parking spaces on the south side of Hector Park? Thank you very much!"

RV: "Commissioner Sorensen: As requested, we will remove the parking spaces from the park."

April 29, 2021: Mr. Verma to Mark Williams as well as stormwater team and other City personnel

"If you're satisfied that contractor has a valid reason, we'll continue to move forward. My goal is to get out of there ASAP. I'm prepared for any fallout. Can't afford to get into a contest with contractor at this point and get into a lawsuit situation. [Francisco]: Please monitor this aspect as best as you can."

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report

June 4, 2021: Mr. Verma to Ms. Grant and other City personnel

"I am assuming that our conversation after this email went out was helpful. To summarize, the original scope changed significantly (changed every week). There were multiple sub-projects with multiple funding sources in the same area. Following the correct process became impossible due to events beyond staff's control. Most importantly, the deadline of water consent order had to be complied with. All work was done with my approval. Staff simply followed my directions. I had a deadline to meet and move on to other more important projects."

April 5, 2021: Mr. Verma to Commissioner Sorensen and other City personnel including Mr. Lagerbloom and Alain Boileau

"Good afternoon Commissioner: While there is some merit to Fred's comments, with respect, I must disagree. **If we were to follow the full blown process, the project would still have been in the design phase. I have always maintained that certain things would be lacking and missing, which we could reconcile later. Trying to coordinate water, stormwater and sewer projects along with the design changes has been very challenging. There are permitting and contractual limitations that the staff cannot overlook. Our goal has been and continue to be to finish the critical elements first and then make other adjustments.** The landscaping plans were prepared by Tom White, City's landscape architect. We are making alternate arrangements based on the needs and priorities. Hope to have new resources in June 2021." (emphasis added).

As previously indicated, Mr. Verma expressed frustration with the City's policies and procedures. In February 2021, Mr. Verma handed a resignation letter to Mr. Lagerbloom, which he later rescinded. Mr. Verma ultimately resigned on or around June 18, 2021 with July 7, 2021 as his effective termination date. In his resignation letter, Mr. Verma provided his criticisms of the City including the "demanding (and many times unrealistic) expectations of the Community and Commission."

During our review, we also noted the following e-mail excerpt between Ms. Hart and Ms. Holcombe regarding paying a vendor. This e-mail appears to suggest that the City may not have complied with its policies and procedures in relation to other projects.

March 10, 2020: Series of e-mails between Ms. Hart to Ms. Holcombe and other City personnel

JH: "Where are we at with getting a po [purchase order] [for] the Rio Vista emergencies?"

KH: "We have the requisitions started in BSO, however funding is not available until the 3/17 Commission consideration of the necessary budget amendment."

JH: "How can we get creative? The vendor should not have to wait until commission. They have already provided the service. Can we juggle in the meantime?"

Finding 4

Internal Control Override Analysis – Public Works Director

The City's policies and procedures state that "no officer of the city shall, except in cases of emergency as specified herein, issue any oral or written purchase order, contract, or conduct open market purchases in any manner unless specifically authorized by this article." The City's policies and procedures further defines an unauthorized purchase as "any item(s) or service(s) that is purchased in a manner that is inconsistent with this article or the Procurement Manual, including any item or service that is: Purchased without sufficient funds; Splitting orders, [etc.]." Based on the foregoing information, it is clear that Mr. Verma knowingly overrode the City's policies and procedures on the Rio Vista Restoration Project. Mr. Verma knowingly directed the stormwater team to bypass the City's policies and procedures as well. It does not appear that Mr. Verma maliciously overrode the City's policies and procedures or received a personal benefit from these overrides.

In certain correspondences, the City Manager and other City personnel were copied regarding additions to the project's scope. These personnel have indicated that they were unaware of Mr. Verma's direction to override City policies and procedures. Due to the minimal amount of correspondence that these individuals were copied on in relation to the internal control overrides, it is unlikely that these individuals were aware of the internal control overrides at the time.

During our review of the Public Works Director's electronic data, we noted various admonishment to various Public Works personnel regarding their contacting/involving other departments, like Procurement, without discussing with Mr. Verma first. Mr. Verma also regularly expressed frustration with the City's policies and procedures to Public Works personnel and others within and outside the City. Although Mr. Verma may have had well-intended purposes behind these admonishments and expressions of frustration, it may have also caused a failure or a poor "tone at the top" in the Public Works Department. Per the National Commission on Fraudulent Reporting, the "[t]one at the top refers to the ethical atmosphere that is created in the workplace by the organization's leadership. Whatever tone management sets will have a trickle-down effect on employees of the company. If the tone set by managers upholds ethics and integrity, employees will be more inclined to uphold those same values. However, if upper management appears unconcerned with ethics and focuses solely on the bottom line, employees will be more prone to commit fraud because they feel that ethical conduct is not a focus or priority within the organization. Employees pay close attention to the behavior and actions of their bosses, and they follow their lead. In short, employees will do what they witness their bosses doing." The National Commission on Fraudulent Reporting has also determined that the tone at the top has a significant role in creating an anti-fraudulent or fraudulent atmosphere.

We noted various e-mails where the stormwater team also expressed frustration with the procurement process. These frustrations, combined with the lack of reporting internal control overrides or refusal to override internal controls, supports the determination that there was a failure in the "tone at the top" of the Public Works Department. Certain City personnel indicated that the City's policies and procedures are adequate and there was just a failure to follow policies and procedures by certain City personnel.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report

Mr. Verma also in effect created an opportunity for Commissioner Sorensen to direct City personnel. This opportunity was in part created by Mr. Verma continually directing his staff to directly correspond with Commissioner Sorensen. It also appears that Mr. Verma did not intervene or request the City Manager to intervene in Commissioner Sorensen's involvement when the stormwater team complained about the level of correspondence from Commissioner Sorensen.

Internal Control Override Analysis – Commissioner Directives

The City Charter governs the roles, responsibilities and prohibitions of the City Commission and the Charter Officers. Specifically, Section 3.07 of the City Charter states the following:

“Neither the city commission nor any of its members shall direct the appointment of any person to office or employment by the city manager, or in any manner prevent the city manager from using his or her own judgment in selecting those officers or employees which he or she is entitled to appoint or select under provisions of this charter, and the civil service system rules and regulations. **Except for the purpose of inquiry, the commission and its members shall deal with the administrative service solely through the city manager, and neither the commission nor any member thereof shall give orders to any subordinates of the city manager, either publicly or privately.**” (emphasis added).

Section 6.06 of the City Charter further provides the following:

“Neither the city commission, any of its committees, nor any of its members, individually or collectively, shall direct the appointment of any person to, or removal from, office by the city manager or any of the manager's subordinates, or in any manner, directly or indirectly, take part in the appointment or removal of any officer or employee in the classified or nonclassified service of the city except as provided in section 6.02 of this article. All inquiry dealing with any portion of the classified or nonclassified service of the city shall be with the city manager, except with regard to assistant city clerks, assistant city auditors, and except with regard to commission assistants, **neither the city commission nor any member thereof shall give any orders to any subordinate or officer of the city, either publicly or privately, directly or indirectly. Any violation of the provisions of this section by a member of the city commission shall be grounds for removal from office.**” (emphasis added).

Based on the foregoing information, certain communications from Commissioner Sorensen to the stormwater team by themselves appear to be Commission inquiry only. However, based on the volume and frequency of Commissioner Sorensen's communications with the stormwater team, even when put in the form of an inquiry, Commissioner Sorensen in effect directed City staff during the Rio Vista Restoration Project. In addition, other communications from Commissioner Sorensen do not appear to be mere inquiries, but instead provide direction to City personnel and City vendors. This direction appears to be contrary to the City Charter. It does not appear that Commissioner Sorensen gave such direction with malicious intent nor did he receive monetary benefits related to the Rio Vista Restoration Project.

Conclusion

Based on the aforementioned observations and findings, the City should consider implementing the following recommendations for improving its internal controls:

1. Change Order Approvals

Finding: There appears to be inconsistencies regarding the City's interpretation of its procurement policies and procedures as they relate to change orders and task orders.

Effect: The City may not be in compliance with its policies and procedures.

Recommendation: The City should review its procurement policies and procedures for clarity. The City should provide additional training to relevant personnel regarding change orders and task orders.

2. Continuing Contracts

Finding: The City appears to have taken conflicting interpretations regarding the administrative renewal of its continuing contracts and whether the administrative renewal provides for additional funding without City Commission approval.

Effect: The City may be awarding additional funds to continuing contracts without proper approval.

Recommendation: The City should review its procurement policies and procedures as well as its contracts for clarity regarding administrative contract renewals. The City should provide the relevant personnel with training regarding any changes to its interpretation.

3. Commission Inquiries

Finding: A City Commissioner directed City personnel and City vendors.

Effect: The City may not be in compliance with its City Charter.

Recommendation: The City should provide additional guidance to the City Commission and City personnel regarding what is considered appropriate inquiries and interaction with lower level staff.

4. Tone at the Top

Finding: There was a failure in the tone at the top of the Public Works Department.

Effect: The poor tone at the top in part resulted in overrides to City policies and procedures.

Recommendation: The City should provide appropriate guidance including whistleblower provisions to its personnel regarding reporting potential internal control overrides.

5. Public Records

Finding: The City was unaware of the existence of certain communications by Commissioner Sorensen related to City business.

Effect: The City may not be in compliance with Florida Statutes regarding public records retention.

Recommendation: The City should review its policies and procedures related to public records retention for adequacy and provide appropriate training, where necessary.



**City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Report**

Based upon the foregoing information, the former Public Works Department Director, Raj Verma, knowingly overrode the City's policies and procedures on the Rio Vista Restoration Project. Mr. Verma directed Mr. Castellon, Mr. Petrica and Mr. Rios to bypass/override the City's policies and procedures as well. These individuals did not report these internal control overrides. These overrides were in part caused by Commissioner Sorensen's direction of certain City personnel and certain City vendors. Mr. Verma did not address Commissioner Sorensen's direction and/or did not report this issue to the City Manager.

These failures/overrides allowed unapproved/unauthorized additions to the Rio Vista Restoration Project's scope. Mr. Verma's actions and inactions also created a poor "tone at the top" within the Public Works Department. The City was unaware of certain communications from Commission Sorensen related to City business that appeared to be stored on Commissioner Sorensen's personal cell phone. As such, the City may not be retaining certain City records in accordance with Florida Statutes on public records retention.

The City has taken broad or conflicting interpretations on the administrative renewal of master contracts as well as the uses of master contracts. This appears to have included administratively renewing contracts for additional funds not clearly authorized by the City Commission. The City has also utilized line item master contracts for unrelated projects not included in the master contract scope. The interpretations appear to have occurred from prior City administrations and the City has utilized these interpretations as the basis for some of its procurement decisions.

City Management reviewed and concurred with CRI's recommendations, which are delineated in this report. Per the City Manager, the City is taking the necessary steps to implement these recommendations. The City has also hired a new Public Works Director, who will focus on creating an ethics driven organizational culture.

Supplementary Information

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
04/06/20	Commissioner Sorensen	Raj Verma and Resident	Raj, Grande Drive east of Eisenhower - water project - Port Watermain Project. Can you give us an update?
04/06/20	Raj Verma	Commissioner Sorensen; Resident; and, Omar Castellon	Omar: Please provide an update. Thanks Raj
06/17/20	Commissioner Sorensen	Raj Verma; Dr. Nancy Gassman; and, Rio Vista Resident	Raj and Nancy, Can we remove this boom? Thank you. Ben
07/01/20	Commissioner Sorensen	Rio Vista Residents; Raj Verma; and, Dr. Nancy Gassman	Let's check on these items. Raj, Nancy and Anthony, Can you help with or point us in the right direction for Mary's questions? We have been trying to get her sidewalk fixed since the beginning of the year. Her sidewalk was broken in multiple pieces and removed due to the work on the sewage break. Thank you!
07/23/20	Commissioner Sorensen	Raj Verma	Forwarded Rio Vista Resident e-mail regarding sidewalk and road repairs.
07/29/20	Commissioner Sorensen	Francisco Rios; Rio Vista Residents; and, David Mancini, Jr.	City Team and David, Can you give us your feedback to Beth's questions?
07/29/20	Raj Verma	Commissioner Sorensen; Francisco Rios; Omar Castellon; and, Thomas White	Except for Tarpon River cleanup/dredging question, please provide Beth a timeline. May be we can put the timeline on our webpage. For that, please have Omar coordinate with Chaz.
07/29/20	Commissioner Sorensen	Rio Vista Resident and Raj Verma	Thank you for your email. We will immediately look into this. Raj, Can you please see below?

See Forensic Examination Report.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
09/28/20	Commissioner Sorensen	Raj Verma; Dr. Nancy Gassman; and, Rio Vista Resident	Hi Raj and Nancy, Can you look I to the below? Thanks Hey Ben, just FYI there is a lot of nasty looking water in the Tarpon just east and west of the 9th ave bridge, don't know if it is from construction in hector park.
10/13/20	Commissioner Sorensen	Christina Currie; Francisco Rios; Raj Verma; Omar Castellon; Thomas White; and, Rio Vista Residents	Team, I just had a good talk with Francisco and it sounds like we will be able to have the trees protected with the guidance of the city arborist this week. Ben
10/21/20	Commissioner Sorensen	Dr. Nancy Gassman; Francisco Rios; Rares Petrica; Marie Pierce; and, Rio Vista Resident	Thanks. We will look into this. Nancy and Francisco, Can you please see below?
10/21/20	Dr. Nancy Gassman	Commissioner Sorensen; Francisco Rios; Rares Petrica; Marie Pierce; and, Rio Vista Resident	Stormwater Operations inspectors will be reviewing the situation today. By his email, Commissioner Sorenson has also asked Engineering to review construction projects in the area.
10/21/20	Francisco Rios	Commissioner Sorensen; Dr. Nancy Gassman; Rares Petrica; Marie Pierce; and, Rio Vista Resident	The contractor working on Hector Park will send a crew crew to check the storm drains as soon as possible. If they have to remove any erosion control devices to make sure the houses don't get flooded, they will do so, and they will install them back after the flooding has subsided.
10/24/20	Commissioner Sorensen	Raj Verma; Ben Rogers; and, Christina Currie	Ben and Raj, Can you give me an update on what I think was a new water pipe that was installed across SE 7th Street between Federal Highway and 616 SE 7 Street? I think the work is done and now it needs to get paved. Thanks! Ben

See Forensic Examination Report.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
10/24/20	Commissioner Sorensen	Christina Currie; Raj Verma; Phil Thornburg; and, Francisco Rios	Let's get an update from Phil and Francisco. Phil, Raj and Francisco, Can you help with Whitney's question and give us an update on Virginia Young Playground progress? Thank you. Ben
10/25/20	Greg Chavarria	Chris Lagerbloom; Ben Rogers; Raj Verma; Tarlesha Smith; and, Commissioner Sorensen	Good evening Commissioner Sorensen: Staff followed up on the inquiry from the Hinterland Group citation that took place this past week. We came to know that the citation was made by our PD for the contractor not violating local ordinance. We were prompted to take action due to a Facebook video post reported by the public. Below is a copy of the citation detail that specifies negligence of not having a weeping bag for the dewatering process. The contractor did not follow process and should know about this local ordinance requirement. Staff feels that citation is fair and just. The citation is local and no other agency is involved. Please let us know if you have any further questions.
11/13/20	Commissioner Sorensen	Francisco Rios	Hi Francisco! Is Hinterland able to start construction on the park on Monday? Thanks! Ben
12/13/20	Commissioner Sorensen	Resident; Raj Verma; and, Ben Rogers	I am sorry about this. Raj and/or Ben, Could you please help me? Thank you. Ben
12/13/20	Raj Verma	Resident; Ben Rogers; Commissioner Sorensen; Omar Castellon; and, Alex Torres	Sure Commissioner. Copying Omar and PM, Alex. Thanks Raj

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
12/16/20	Commissioner Sorensen	Rio Vista Resident; Christina Currie; and, Omar Castellon	Thank you for all of your patience in dealing with all of this. Omar, Can you give us an update and also give us an idea of when Ponce De Leon might be paved? Thank you. Ben
01/07/21	Commissioner Sorensen	Rio Vista Residents; Raj Verma; and, Omar Castellon	Thanks so much for these additions and sharing the concern about the dirt mountains. Raj and Omar, When can the dirt be leveled? Thank you. Ben
01/07/21	Raj Verma	Omar Castellon; Francisco Rios; and, Victor Carosi	Can we have temporary asphalt until we are ready to mill and pave the whole road? It would be a CO but that would be fine. Thanks

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
01/14/21	Commissioner Sorensen	Rio Vista Residents; Francisco Rios; Raj Verma; Omar Castellon; and, Christina Currie	<p>I was at Hector Park yesterday meeting with Jimmy with Hinterland...knocking on some of your doors to provide an update. Hinterland is installing a water main under the street on the north side of Ponce de Leon...They should have finished last night the work in front of your house Stephanie and should be working in front of your house today Strawn. The will continue moving east installing the water main. Additionally, we are going to be installing a new stormwater pipe and re-grading the street to help with drainage. Francisco and I were talking about this yesterday. I would like the water main and the stormwater pipe done at the same time but we are waiting on further engineering work for the stormwater pipe.</p> <p>The big piles of excavated materials that had been stored on the northeast corner of Hector Park, have been hauled off from the site. There is still some construction material remaining that will be used to backfill the trench for the new watermain. Those piles would have to remain on-site, but I will have the contractor move them further away from the fence so the material doesn't spill over onto the roadway.</p> <p>Omar, Can you give us a new update? Thank you!</p>
01/16/21	Commissioner Sorensen	Francisco Rios and Rio Vista Resident	<p>Francisco will make sure this can work. If you have any issues just call me on my cell - 954.218.3688. Have a great trip! Thank you!</p> <p>Ben</p>
01/26/21	Commissioner Sorensen	Rio Vista Residents; Raj Verma; Omar Castellon; and, Francisco Rios	<p>Good question. Francisco and Omar, Is there anything that can be done about this FPL pole Strawn mentions below? Thanks.</p> <p>Ben</p>

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
01/29/21	Commissioner Sorensen	Raj Verma	SW 15 Court has a clogged drain - I think. Can we look into this? Thank you! Ben
02/02/21	Commissioner Sorensen	Rio Vista Resident; Christina Currie; Francisco Rios; and, Ben Rogers	Ben Rogers, Can we explore putting in two permanent speed bumps on SE 11 Street (on the south side of Hector Park)? There was one there before this road/sewer work was done. Also, can we explore slightly narrowing SE 11 Street there as well, adding more space to the park? Thank you!
02/05/21	Raj Verma	Commissioner Sorensen; Rio Vista Residents; Francisco Rios; Omar Castellon; Chris Lagerbloom; Christina Currie; and, Victor Carosi	I checked out the project site yesterday. Yes, we can narrow the road to about 11'. For consistency's sake (to match the pattern on the west side of SE 9th Avenue and to restore what was there before), we recommend 4-foot bike lanes (striped) on both sides of Hector Park. Speed humps are desirable because of "straight shot" roadway. I'm not sure what process the City has for Residethood support to get them. I will need help / recommendation from the HOA, including the locations. Thanks

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
02/05/21	Commissioner Sorensen	Raj Verma; Rio Vista Residents; Francisco Rios; Omar Castellon; Chris Lagerbloom; Christina Currie; and, Victor Carosi	Thank you very much. That is great news about narrowing the road and the speed humps! When you say we can narrow SE 11 Street to 11 feet, does that 11 feet include the 4 foot wide bike lane or is it 11 feet plus a 4 foot wide bike lane for a total of 15 feet? I would prefer a total width of 11 feet. Christina (President of Rio Vista Civic Association), Is the narrowing of the street okay from a Civic Association perspective? In terms of the location of speed humps on SE 11 Street, I have been talking with the Residents on SE 11 Street about locations. Is that process of determining the location along with Raj okay or do you have a process preference?
02/05/21	Raj Verma	Commissioner Sorensen; Rio Vista Residents; Francisco Rios; Omar Castellon; Chris Lagerbloom; Christina Currie; and, Victor Carosi	It is 11' (lane width) + 4' bike lane. Absolute minimum lane width is about 9' to 10' per Code/Design Standards provided there is no room. Preferable width is 10' to 11' Thanks
02/05/21	Commissioner Sorensen	Raj Verma; Rio Vista Residents; Francisco Rios; Omar Castellon; Chris Lagerbloom; Christina Currie; and, Victor Carosi	Residents, I just spoke to Raj and we believe we have flexibility to have or not have bike lanes. So, let's do this. How about we all meet onsite with Raj on SE 11 Street at Hector Park on Monday (2/8) at 4 PM? We can review all options and put forward our preferred option? Ben

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
02/09/21	Commissioner Sorensen	Rio Vista Residents; Raj Verma; Francisco Rios; and, Rares Petrica	We will look into this. Those sidewalks look horrible. Raj, Rares and Francisco, Can we have these sidewalks fixed as part of our post-sewer work? Thank you.
02/09/21	Raj Verma	Commissioner Sorensen; Rio Vista Residents; Francisco Rios; and, Rares Petrica	All sidewalks damaged during the projects will be fixed. Thanks
02/10/21	Rares Petrica	Francisco Rios	Can we please make sure Hinterland replaces these flags of sidewalk.
02/22/21	Commissioner Sorensen	Rio Vista Resident; and, Francisco Rios	We are working on it [playground equipment]. Francisco, Can you give us an update? Thanks!
03/08/21	Commissioner Sorensen	Francisco Rios; Rio Vista Residents; Rares Petrica; and, Omar Castellon	All good questions. Omar, Francisco and Rares, Can you help us with Al's questions? Thank you. Ben
03/19/21	Commissioner Sorensen	Francisco Rios; Rio Vista Residents; Rares Petrica; and, Omar Castellon	Francisco, Is the contractor working today and this upcoming week in the Hector Park area? I just wanted to check to ensure they are going to be pushing hard to complete everything. Thanks! Ben
04/23/21	Commissioner Sorensen	Francisco Rios and Rio Vista Resident	I think so. Francisco, I would like it to be an individual choice for each homeowner. Can you confirm? Thanks Ben

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
04/23/21	Commissioner Sorensen	Rio Vista Residents; Omar Castellon; Francisco Rios; Alex Torres; and, Raj Verma	I am not sure but let's ask. Francisco, Can you help with Chris' questions regarding "There is additional underground infrastructure repair/replacement on Ponce de Leon Drive, as part of a different project, which might impact the dates shown.)"? Thanks! Ben
04/30/21	Commissioner Sorensen	Rio Vista Residents; Francisco Rios; and, Rares Petrica	Let's gets some feedback from Francisco and Rares. Rares and Francisco, Please see below.
04/30/21	Rares Petrica	Rio Vista Residents; Francisco Rios; and, Commissioner Sorensen	The contractor will remove the filter fabric this morning from the catch basin which will drain the area, the fabric is required as pollution prevention measure.
05/06/21	Rares Petrica	Francisco Rios	Can you send Ben Sorensen and cc me and Raj that light poles that we calling out for Virginia Park, and if any for Hector.
05/06/21	Francisco Rios	Commissioner Sorensen; Raj Verma; and, Rares Petrica	Good afternoon Commissioner Sorensen: Please see attached shop drawings for the new light posts and fixtures. There will be three (3) light posts installed at Virginia Young Park, around the new playground area. No light posts are proposed at Hector Park.
05/07/21	Christina Currie	Commissioner Sorensen	I like that they have the anti-graffiti coating. If possible I think adding the outdoor electric outlets at bottom like some others around the City have would be useful for cellphone charging and maybe even lights at holiday time.
05/07/21	Commissioner Sorensen	Christina Currie; Rares Petrica; and, Francisco Rios	Rares and Francisco, Can you give us feedback on Christina's idea? Thanks

See Forensic Examination Report.

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Schedule A - Summary of Relevant Communications

Date	From	To	Applicable Correspondence (Emphasis in Bold)
06/03/21	Commissioner Sorensen	Rio Vista Residents; Omar Castellon; Francisco Rios; and, Alex Torres	Rares or Francisco, Can you give us an update on Hector and Virginia Young Parks? Ben
06/12/21	Commissioner Sorensen	Raj Verma; Rares Petrica; and, Anthony Fajardo	Hi team Sidewalk blocked off at 1002 E las Olas where city did water tap. Been that way for a couple weeks. Would be very good if it got repaired and opened back up. I think it is city but not sure. Is this us? Can we complete it? Ben
06/15/21	Commissioner Sorensen	Rares Petrica	Rares, Are we working on that pipe at the Animal Hospital? Also, can you give me a quick update on the Rio Vista parks? Ben
06/23/21	Commissioner Sorensen	Francisco Rios; Rio Vista Residents; Rares Petrica; and, Omar Castellon	Francisco, Rares and Omar, Thanks in advance for the update. Ben

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Appendix A – Expert Qualifications



Ben Kincaid, CPA, CFE, CFF, CVA
Partner in the Forensic, Litigation and Valuation Services Group
(850) 837-3141 phone | BKincaid@CRIcpa.com

Experience

Known for his data analytics and translating the data into defensible, investigative results, Ben Kincaid has over nine years of experience in providing forensic accounting, litigation support and business valuation services across CRI's footprint. These services have included investigating compliance, employee malfeasance, hidden asset schemes, breach of contract claims, business interruption losses, economic damages, due diligence and valuation disputes. Ben has provided these services to a wide range of clients and industries; such as, state, county and local governments as well as private companies, non-profit organizations and publicly traded companies.

Ben speaks regularly on the topics of fraud prevention, fraud detection and business valuations. Ben has also worked with various law firms and law enforcement on civil and criminal matters and presented findings to various law enforcement agencies including the FBI, FDLE, DOJ and GBI. Ben also provides expert witness services and has qualified as an expert witness in various state courts. Ben is a graduate from Pensacola Christian College with a Bachelor of Science Degree in Business with a double concentration in Accounting and Finance. Ben serves on the FICPA's Valuation, Forensic Accounting and Litigation Committee and is a deacon at his church.

Education, Licenses & Certifications

- BS, Business, Pensacola Christian College
- Certified Public Accountant (CPA) – Indiana and Florida
- Certified Fraud Examiner (CFE)
- Certified Valuation Analyst (CVA)
- Certified in Financial Forensics (CFF)

Professional Affiliations

- American Institute of Certified Public Accountants (AICPA)
- Florida Institute of Certified Public Accountants (FICPA)
- Association of Certified Fraud Examiners (ACFE)
- National Association of Certified Valuators and Analysts (NACVA)

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Appendix A – Expert Qualifications



Rob Broline, CPA
Partner in the Forensic, Litigation and Valuation Services Group
(321) 426-3026 phone | RBroline@CRLcpa.com

Experience

Rob has over twenty years of proven skills and experience in public accounting. Industries served include the following: K-12, Higher Education, State and Local government, Hospitality, Healthcare, Construction, and Commercial. Rob specializes in entity-wide risk assessments, process risk / controls assessments, internal audits, operational audits, construction cost audits and forensic reviews. Rob is the CRI lead on the outsourced internal audit work that CRI performs for the Brevard County Board of County Commissioners. Internal and operational audits performed include, but are not limited to, the following departments / functions: accounts payable; central services; community block development grant; facilities; information technology; parks and recreation; public works; purchasing cards; asset management; central cashier; fire rescue; licensing, regulation, and enforcement; purchasing and procurement; timekeeping and overtime.

Education, Licenses & Certifications

- BA, Accounting, Cedarville University
- Certified Public Accountant (CPA)
- Certified Construction Auditor

Professional Affiliations

- American Institute of Certified Public Accountants (AICPA)
- Florida Institute of Certified Public Accountants (FICPA)
- Institute of Internal Auditors
- Speaker Florida Government Finance Officers Association
- Speaker Government Finance Officers Association National Conference

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Appendix A – Expert Qualifications



Steve Riggs, CPA, Cr.FA

Partner in the Forensic, Litigation and Valuation Services Group

(850) 837-3141 phone

SRiggs@CRIcpa.com

Experience

Steve Riggs has over 40 years of experience in public accounting and consulting services. He specializes in taxation, representation before the Internal Revenue Service (IRS), divorce settlements and litigation, forensic accounting, mergers and acquisitions, and court appointed corporate/trustee engagements. In January 2009, Steve was appointed to the Florida Board of Accountancy. Steve also served as Chairman of the Florida Board of Accountancy in 2014.

Steve is a founding partner of one of the top 25 accounting firms in the country, Carr, Riggs & Ingram, LLC (CRI). CRI employs more than 1,800 professionals in 43 offices across Alabama, Florida, Georgia, Kentucky, Louisiana, Mississippi, North Carolina, Tennessee, New Mexico and Texas. Prior to co-founding Carr, Riggs & Ingram, Steve worked for the IRS as a field agent for four years in Jacksonville, Florida.

Steve has been appointed by various Courts as a corporate trustee or custodian and has managed and sold businesses under the supervision of the Court. Steve has also been appointed by the Courts as an expert witness and as an executor.

Steve is a graduate from the University of West Florida in Pensacola with a bachelor's degree in accounting. Today, Steve serves on the University of West Florida College of Business Advisory Council and the Board of Trustees of the University of West Florida Foundation.

Education, Licenses & Certifications

- BS, Accounting, University of West Florida
- Certified Public Accountant (CPA)
- Certified Forensic Accountant (Cr.FA)

Professional Affiliations

- American Institute of Certified Public Accountants
- Florida Institute of Certified Public Accountants
- Alabama Society of Certified Public Accountants
- American Board of Forensic Accounting

City of Fort Lauderdale, Florida
Rio Vista Restoration Project
Forensic Examination Supplementary Information
Appendix B – Source Documentation

We reviewed and relied upon the following documentation during our investigation:

- City Charter;
- City Manager Memorandum No. 21-35, Management Responses;
- Procurement Ordinance;
- Procurement Manual including revisions;
- Public Works Department Organizational Charts;
- Jodi Hart Resignation Letter;
- Raj Verma Resignation Letter;
- Various Notice to Proceed/Contractors/Owner;
- Desk phone call logs for James Hemphill, Chris Lagerbloom, Ben Sorensen, Jodi Hart, Susan Grant, Francisco Rios, Kymberly Holcombe, Marie Pierce, Raj Verma, Thomas Williams, Nancy Gassman, Talal Abi-Karam, Rares Petrica, Phil Thornburg, Victor Carosi, Omar Castellon and Elkin Diaz;
- City cell phone call logs for Ben Sorensen, Chris Lagerbloom, Kymberly Holcombe, Nancy Gassman, Raj Verma and Victor Carosi;
- Relevant City e-mails for James Hemphill, Chris Lagerbloom, Ben Sorensen, Jodi Hart, Susan Grant, Francisco Rios, Kymberly Holcombe, Marie Pierce, Raj Verma, Thomas Williams, Nancy Gassman, Talal Abi-Karam, Rares Petrica, Phil Thornburg, Victor Carosi, Omar Castellon and Elkin Diaz;
- Applicable Checks to Hinterland Group, Inc.;
- Applicable Pay Estimates/Applications and Supporting Documentation for Hinterland Group, Inc.;
- Applicable Task Orders, Change Orders and Electronic Approvals for Hinterland Group, Inc.;
- Bid Solicitation for Stormwater Construction Services Contract;
- Stormwater Construction Services Contracts;
- Applicable Commission Agenda Memorandums and Supporting Documentation; and,
- Various Public Works Data Related to Hinterland Group, Inc.



Memorandum

Memorandum No: 21-38

Date: November 22, 2021

To: John Herbst, City Auditor

From: Chris Lagerbloom, ICMA-CM, City Manager

Re: Forensic Examination of the Rio Vista Restoration Project – Management Responses

A handwritten signature in blue ink, appearing to read "CLagerbloom".

Management appreciates the City Auditor making the Forensic Examination of the Rio Vista Restoration Project a priority. The examination identified Findings that will be addressed by Management.

The following are Management Responses to the examination Findings:

Finding 1

Change Order Approvals

Finding: There appears to be inconsistencies regarding the City's interpretation of its procurement policies and procedures as they relate to change orders and task orders.

Recommendation: The City should review its procurement policies and procedures for clarity. The City should provide additional training to relevant personnel regarding change orders and task orders.

Management Response: *Management concurs with the recommendation. The Procurement Code and Manual will be reviewed to provide specificity and consistency with regard to eligible expenditures in task orders and change orders. Additional training will be provided to Procurement staff as well as staff charged with administering contracts in using Departments.*

Finding 2

Continuing Contracts

Finding: The City appears to have taken conflicting interpretations regarding the administrative renewal of its continuing contracts and whether the administrative renewal provides for additional funding without City Commission approval.

Recommendation: The City should review its procurement policies and procedures as well as its contracts for clarity regarding administrative contract renewals. The City should provide the relevant personnel with training regarding any changes to its interpretation.

Memorandum No: 21-38
Page 2 of 3

Management Response: *Management concurs with the recommendation. The Procurement Code and Manual will be reviewed to provide specificity and consistency with regard to the dollar value of administrative renewals. Additional training will be provided to Procurement staff as well as staff charged with administering contracts in using Departments. Public Works will coordinate training on proper use of Continuing Contracts with the Procurement division to ensure all Project Management staff understand the related procurement policies.*

Finding 3 *Commission Inquiries*

Finding: A City Commissioner directed City personnel and City vendors.

Recommendation: The City should provide further guidance to the City Commission and City personnel regarding what is considered appropriate inquiries and interaction with lower level staff.

Management Response: *A memorandum will be provided to all Public Works staff highlighting Section 3.07 and 6.06 of the City Charter and providing guidance on the difference between an inquiry and a directive and the appropriate response should they receive a request from a Commissioner. Public Works leadership will ensure any requests are directed through proper channels in the City Manager's Office. In addition to this focused approach in the Public Works Department, a memorandum reminder will be delivered city wide to all employees and questions will be answered as they are raised.*

Finding 4 *Tone at the Top*

Finding: There was a failure in the tone at the top of the Public Works Department.

Recommendation: The City should provide appropriate guidance including whistleblower provisions to its personnel regarding reporting potential internal control overrides.

Management Response: *Management agrees there was a failure at the top of the Public Works Department. When the Finance Director identified the procurement discrepancy and brought it to the attention of the City Manager, a discussion with then Public Works Director Raj Verma, the Human Resources Director, City Attorney and City Auditor occurred on June 17, 2021. Mr. Verma resigned June 18, 2021. The City has hired a new Public Works Director who will focus on creating an ethics driven organizational culture. Furthermore, the Public Works Department will work with the Human Resources Department to identify appropriate training related to internal control overrides and whistleblower provisions to be given to employees. The City has also hired a new Chief Procurement Officer who is very experienced and will provide excellent oversight going forward of our procurement processes.*

Memorandum No: 21-38
Page 3 of 3

Finding 5
Public Records

Finding: The City was unaware of the existence of certain communications by Commissioner Sorensen related to City business.

Recommendation: The City should review its policies and procedures related to public records retention for adequacy and provide appropriate training, where necessary.

Management Response: *Management concurs with the recommendation. A review of policies and procedures related to public records retention will be conducted jointly with the City Clerk and City Attorney. Where necessary, additional training will be provided.*
